Activity ID	Bid Item	211080 - Group	Activity Name	OD	Start	Finish	Total Float
I-5 Hammer LN				971d	Jun-16-11	May-15-...	0d
General Conditions				971d	Jun-16-11	May-15...	0d
A1000			Contract Approval	0d	Jun-16-11*		-1d
A1300			Notice to Proceed	55d	Jun-16-11	Aug-13-...	-1d
A1010			Mobilization	20d	Jul-15-11	Aug-11-...	1d
A1030			Begin Construction	0d	Aug-15-11		0d
A2460			Construction Duration	871d	Aug-15-11	Feb-19-...	0d
A6920			Final Punch List	15d	Feb-04-15	Feb-26-...	0d
A1040			Project Completion	0d		Feb-19-...	59d
A1240			Contractor Owned Float	54d	Feb-27-15	May-14...	0d
A1220			Contract Completion	0d		May-15...	0d
A1420			State Owned Float	0d	May-15-15	May-15...	0d
Submittals				45d	Jun-16-11	Aug-18-...	271d
A1250		RLB	Submit SWPPP to CAL...	20d	Jun-16-11	Jul-09-11	75d
A1260		RLB	Submit Baseline CPM	20d	Jun-16-11	Jul-09-11	14d
A1470		RLB	Submit Water Access	35d	Jun-16-11	Jul-24-11	18d
A1410		RLB	Submit CIDH Plan	37d	Jun-16-11	Jul-26-11	27d
A2100		RLB	Submit CRCP Mix Desi...	60d	Jun-16-11	Aug-18-...	398d
A2120		RLB	Submit Irrigation Cost B...	15d	Jun-16-11	Jul-04-11	34d
A2230		RLB	Submit Electrical Cost ...	15d	Jun-16-11	Jul-04-11	34d
A2310		RLB	Submit Falsework Desig...	40d	Jun-16-11	Jul-29-11	54d
A2500		RLB	Submit Falsework Desig...	40d	Jun-16-11	Jul-29-11	355d
A2510		RLB	Submit Creek Diversion...	35d	Jun-16-11	Jul-24-11	259d
A2520		RLB	Submit Bridge Removal...	30d	Jun-16-11	Jul-19-11	21d
A2660		RLB	Submit Contractor Supp...	18d	Jun-16-11	Jul-12-11	14d
A2670		RLB	Submit NRPP	7d	Jun-16-11	Jun-24-11	20d
A2680		RLB	Submit BRIP	7d	Jun-16-11	Jun-24-11	20d
R/A Submittals				77d	Jun-27-11	Oct-16-11	235d
A8120		CT	NRPP Approved	15d	Jun-27-11	Jul-18-11	20d
A8130		CT	BRIP Approved	15d	Jun-27-11	Jul-18-11	20d
A7630		CT	Irrigation Cost Breakdo...	5d	Jul-05-11	Jul-09-11	34d
A7640		CT	Electrical Cost Breakdo...	5d	Jul-05-11	Jul-09-11	34d
A7320		CT	SWPPP Approved By ...	20d	Jul-10-11	Jul-29-11	75d
A7330		CT	Baseline CPM Approved	20d	Jul-10-11	Jul-29-11	14d
A8110		CT	Contractor Supplied Bio...	10d	Jul-13-11	Jul-26-11	14d
A7900		CT	Bridge Removal Plan A...	21d	Jul-20-11	Aug-09-...	21d
A7890		CT	5 Mile Slough Creek Div...	84d	Jul-25-11	Oct-16-11	259d
A7910		CT	Water Access Approved	10d	Jul-25-11	Aug-05-...	14d
A7600		CT	CIDH Plan Approved	15d	Jul-27-11	Aug-10-...	27d
A7870		CT	14 Mile Slough Falsewo...	21d	Jul-30-11	Aug-19-...	54d
A7880		CT	Calaveras Falsework Pl...	21d	Jul-30-11	Aug-19-...	355d
A7620		CT	CRCP Mix Design and ...	5d	Aug-19-11	Aug-23-...	398d
Pre-Stage 1				17d	Aug-16-11	Sep-08...	23d
A1400	22	FARW	Place Construction Are...	3d	Aug-16-11	Aug-18-...	0d
A1050	104	OCJI	Construct Temporary P...	5d	Aug-18-11	Aug-24-...	0d
A1060		CRSP	Switch Traffic to Stage 1	10d	Aug-25-11	Sep-08...	0d
A1070	45	GERC	Remove Overhead Sign...	10d	Aug-25-11	Sep-08...	23d
Sub Stage 1 - CC to MI				200d	Aug-29-11	Jun-18-12	91d
Roadwork				200d	Aug-29-11	Jun-18-12	91d
A1510	28	RLB	Place K-Rail (Partial)	10d	Aug-29-11	Sep-12...	0d
A2530		SWPP	Install Stage 1 BMP's	10d	Aug-31-11	Sep-14...	19d
A2630	4	RLB	Install Stage 1 ESA Fen...	5d	Sep-09-11	Sep-15...	18d
A2090	75	SOEI	Clear and Grub	10d	Sep-16-11	Sep-29...	18d
A1190	76	RLB	Break and Remove Insi...	2d	Sep-30-11	Oct-03-11	176d
A1200	76	RLB	Break and Remove Insi...	2d	Oct-04-11	Oct-05-11	176d
A1210		RLB	Rough Grade Median - ...	3d	Oct-12-11	Oct-14-11	176d
A1230	101	RLB	Place Class II Base & S...	2d	Oct-17-11	Oct-18-11	228d
A1430		RLB	Fine Grade/Set String Li...	2d	Oct-19-11	Oct-20-11	228d
A1270	104	OCJI	Pave AC Median Sta. ...	1d	Oct-21-11	Oct-21-11	228d
A1280	112	CMCF	Place Rebar - NB Medi...	2d	May-15-12	May-16...	90d
A1380	112	RLB	Pave CRCP NB Media...	5d	May-17-12	May-23...	90d
A1390	112	CMCF	Place Rebar - SB Medi...	2d	May-24-12	May-25...	95d
A1440		CSSI	Cure and Seal CRCP N...	10d	May-24-12	Jun-02-12	131d
A2420		RLB	Profilograph NB CRCP ...	1d	May-24-12	May-24...	101d
A1570	112	RLB	Pave CRCP SB Median...	5d	Jun-04-12	Jun-08-12	91d
A6940		CSSI	Cure and Seal CRCP Fr...	10d	Jun-09-12	Jun-18-12	132d
A2430		RLB	Profilograph SB CRCP ...	1d	Jun-11-12	Jun-11-12	91d
Stage 1				402d	Jul-24-11	Mar-07-...	370d
Roadwork				387d	Aug-15-11	Mar-07-...	370d
A1680	47	RLB	Remove Culvert at Sta. ...	2d	Sep-09-11	Sep-12...	235d
A1580	76	RLB	Break and Remove NB ...	2d	Sep-13-11	Sep-14...	195d

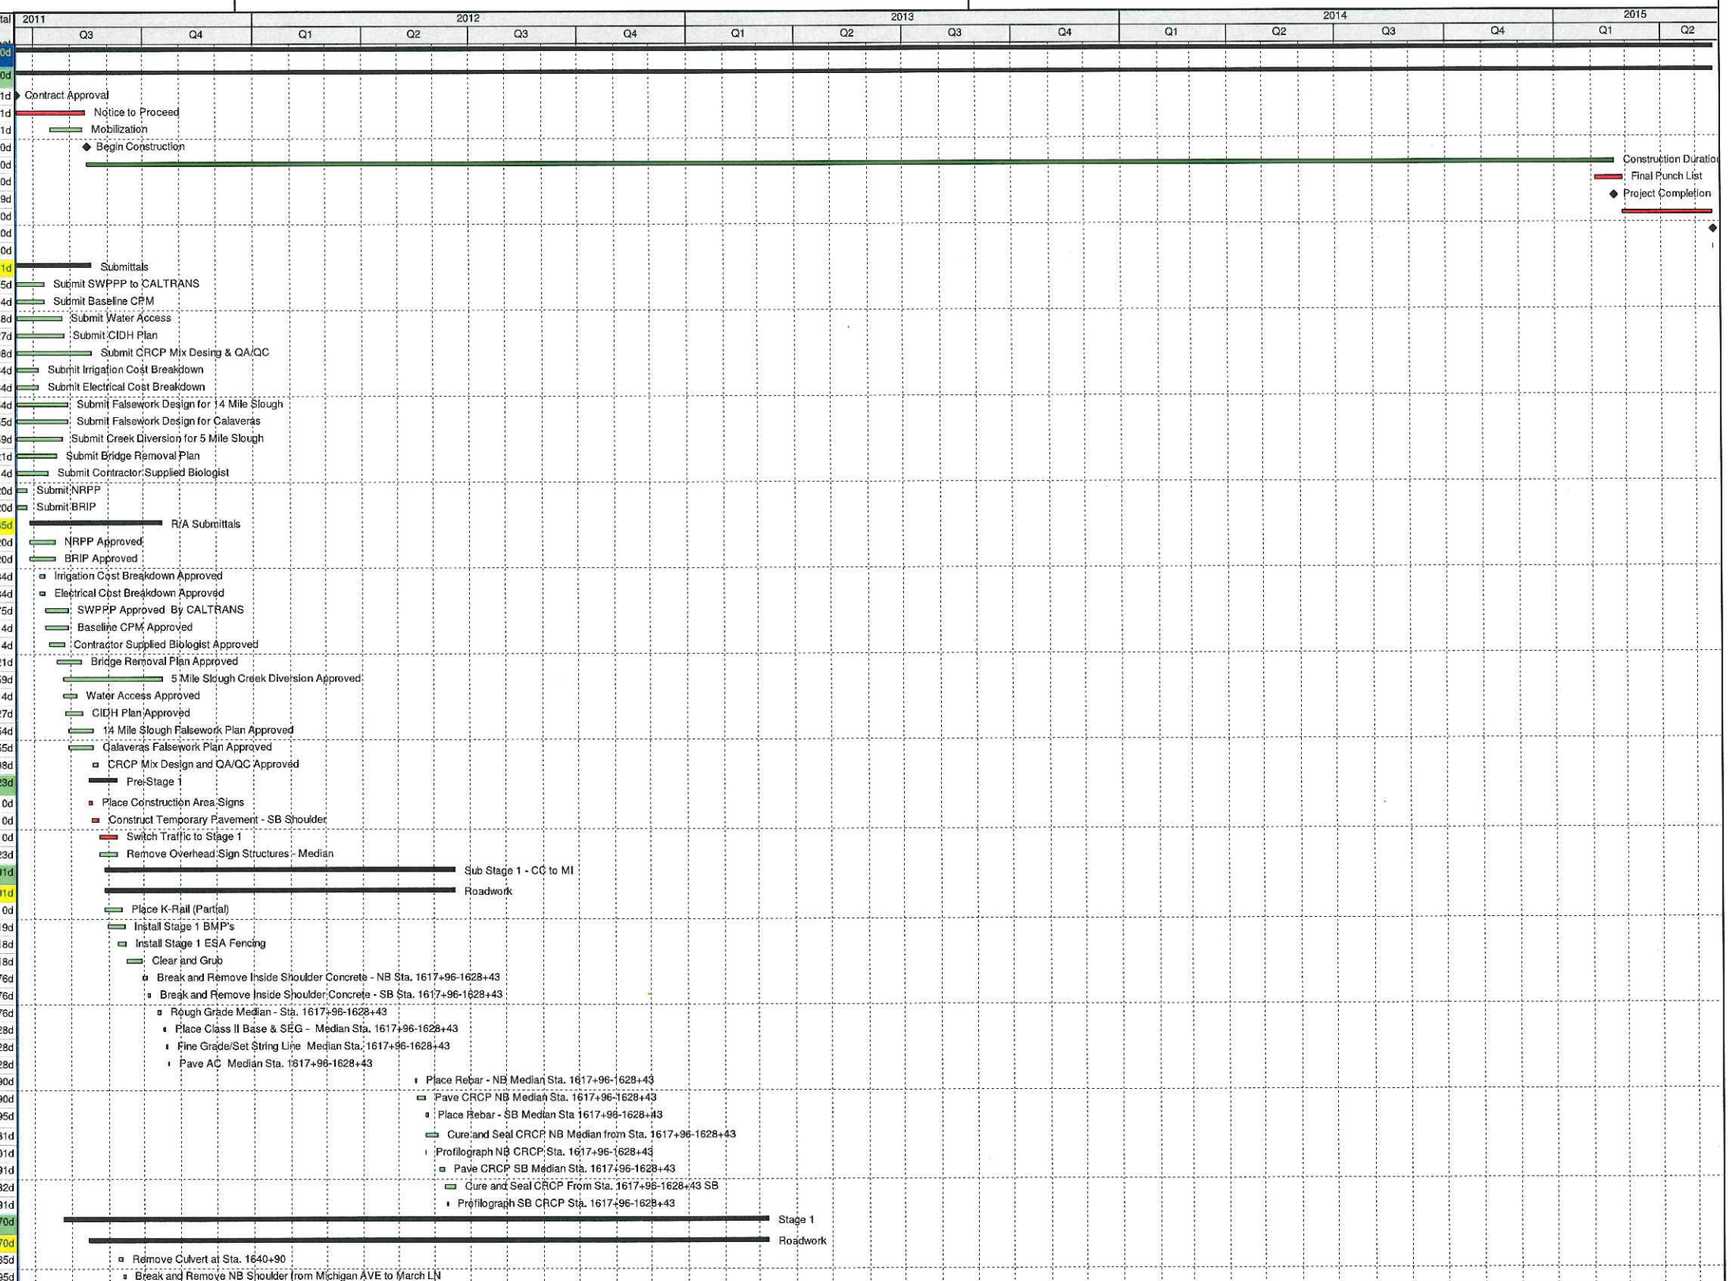

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Start Date: Jun-16-11

Activity ID	Bid Item	211080 - Group	Activity Name	OD	Start	Finish	Total Float
A1590	76	RLB	Break and Remove SB ...	2d	Sep-15-11	Sep-16...	195d
A1600		RLB	Rough Grade Median fr...	25d	Oct-17-11	Nov-21...	176d
A7590	28	RLB	Place K-Rail (Partial) Fr...	10d	Oct-17-11*	Oct-28-11	187d
A7460	76	RLB	Break and Remove NB ...	2d	Oct-31-11	Nov-01...	187d
A7470	76	RLB	Break and Remove SB ...	2d	Nov-02-11	Nov-03...	187d
A1610	101	RLB	Place Class II Base & S...	14d	Nov-21-11	Dec-12...	188d
A7480		RLB	Rough Grade Median fr...	25d	Nov-22-11	Dec-29...	176d
A7490	101	RLB	Place Class II Base & S...	14d	Dec-30-11	Jan-20-12	176d
A1620		RLB	Set Hubs/String Line an...	12d	Mar-01-12	Mar-16-...	134d
A7500		RLB	Set Hubs/String Line an...	12d	Mar-19-12	Apr-03-12	134d
A1630	104	OCJI	Pave AC NB Median fr...	6d	Mar-22-12	Mar-29-...	135d
A1650	112	CMCF	Place Rebar for CRCP ...	4d	May-29-12	Jun-01-12	99d
A7530	112	CMCF	Place Rebar for CRCP ...	4d	Jun-04-12	Jun-07-12	99d
A1660	112	RLB	Pave CRCP - NB Medi...	4d	Aug-01-12	Aug-06-...	56d
A1450		CSSI	Cure and Seal CRCP N...	10d	Aug-07-12	Aug-16-...	184d
A2440		RLB	Profilograph NB Median...	5d	Aug-07-12	Aug-13-...	131d
A7510	104	OCJI	Pave AC NB Median fr...	6d	Aug-28-12	Sep-06...	29d
A7520	104	OCJI	Pave AC SB Median Fr...	5d	Sep-06-12	Sep-13...	29d
A1640	104	OCJI	Pave AC SB Median Fr...	5d	Sep-13-12	Sep-20...	29d
A2570	112	CMCF	Place Rebar for CRCP ...	5d	Sep-20-12	Sep-27...	29d
A7540	112	RLB	Pave CRCP - NB Medi...	4d	Oct-19-12	Oct-24-12	5d
A7550		CSSI	Cure and Seal CRCP N...	10d	Oct-25-12	Nov-03...	105d
A7560	112	CMCF	Place Rebar - SB Medi...	4d	Oct-25-12	Oct-30-12	5d
A7570	112	RLB	Pave CRCP - SB Medi...	4d	Oct-29-12	Nov-01...	5d
A7650		RLB	Profilograph CRCP - N...	3d	Oct-31-12	Nov-02...	74d
A1670	112	RLB	Pave CRCP - SB Medi...	4d	Nov-02-12	Nov-07...	5d
A7660		RLB	Profilograph NB Median...	3d	Nov-02-12	Nov-06...	72d
A7580		CSSI	Cure and Seal CRCP S...	10d	Nov-04-12	Nov-13...	105d
A6930		CSSI	Cure and Seal CRCP S...	10d	Nov-08-12	Nov-17...	101d
A2450		RLB	Profilograph SB Median...	5d	Nov-08-12	Nov-15...	66d
A2060		RLB	Finish Stage 1	0d		Feb-26-...	0d
A2360		CRSP	Switch Traffic to Stage 2A	7d	Feb-27-13	Mar-07-...	0d
In Water Work - 5 Mile Slough				51d	Jul-02-12	Sep-12...	487d
A1760	8	RLB	Install Creek Diversion f...	4d	Jul-02-12*	Jul-06-12	0d
A1180	74	RLB	Demo Portion of Five ...	10d	Jul-09-12	Jul-20-12	163d
A1750		RLB	Excavate for Box Culve...	7d	Jul-26-12	Aug-03-...	163d
A1730	145	RLB	F/R/P Box Culvert @ 5 ...	20d	Aug-06-12	Aug-31-...	163d
A1780	8	RLB	Remove Creek Diversio...	4d	Sep-04-12	Sep-07...	163d
A2000		RLB	Finish Work in 5 Mile SL...	0d		Sep-12...	487d
Road Closures				431d	Aug-15-11	Oct-18-12	29d
A2710			Temporary Closure @ ...	163d	Aug-15-11	Jan-24-12	297d
A2740			Temporary Closure @ ...	172d	Aug-15-11	Feb-02-...	7d
A2760			Temporary Closure @ ...	259d	Feb-03-12	Oct-18-12	7d
Demolition				34d	Aug-31-11	Oct-19-11	192d
A1120	68	HREI	Demo Calaveras Bridge...	3d	Aug-31-11	Sep-02...	0d
A1150	71	HREI	Demo Fourteen Mile Sl...	5d	Sep-06-11	Sep-12...	0d
A1360		RLB	Remove Portion of Sou...	3d	Sep-09-11	Sep-13...	0d
A1080	64	HREI	Demo Country Club Blv...	3d	Sep-13-11	Sep-15...	38d
A1090	65	HREI	Demo Michigan Ave Bri...	3d	Sep-16-11	Sep-20...	58d
A1100	66	HREI	Demo Alpine Ave Bridg...	3d	Sep-21-11	Sep-23...	86d
A1110	67	HREI	Demo Telegraph Ave ...	3d	Sep-26-11	Sep-28...	103d
A1130	69	HREI	Demo EBMUD Bridge ...	5d	Sep-29-11	Oct-05-11	135d
A1140	70	HREI	Demo March LN Bridge...	3d	Oct-06-11	Oct-11-11	148d
A1160	72	HREI	Demo Swain RD Bridge...	3d	Oct-12-11	Oct-14-11	192d
A1170	73	HREI	Demo Benjamin Holt Bri...	3d	Oct-17-11	Oct-19-11	192d
Substructure				265d	Jul-24-11	Aug-14-...	92d
Calaveras River Bridge				89d	Jul-24-11	Dec-01...	268d
In Water Work				70d	Jul-24-11	Nov-01...	287d
A14		RLB	Procure Materials for W...	5d	Jul-24-11	Jul-29-11	27d
A12		RLB	Establish Water Access...	5d	Aug-15-11	Aug-19-...	9d
A20		CASE	Install Permanent CIDH ...	7d	Aug-22-11	Aug-30-...	217d
A13	124	CASE	Install CIDH @ Calaver...	10d	Sep-01-11	Sep-15...	46d
A23		CT	Test CIDH @ Calavera...	20d	Sep-16-11	Oct-14-11	211d
A19	141	RLB	F/R/P Columns and Ca...	10d	Oct-04-11	Oct-18-11	46d
A27		RLB	F/R/P Bent 5A Collumn ...	4d	Oct-19-11	Oct-24-11	211d
A13		RLB	Remove Water Access ...	2d	Oct-25-11	Oct-26-11	46d
A26	206	RLB	Install RSP on South Si...	4d	Oct-27-11	Nov-01...	253d
A70		RLB	Finish Work Bank to Bank	0d		Nov-01...	287d
Out of Water Work				45d	Sep-26-11	Dec-01...	211d
A13	127	CASE	Install CIDH @ Calaver...	16d	Sep-26-11	Oct-18-11	94d
A26		CT	Test CIDH	32d	Sep-28-11	Nov-14...	200d
A23	81	RLB	Excavate Abutment @ ...	5d	Oct-27-11	Nov-02...	211d
A70	141	RLB	F/R/P Collumns and Ca...	12d	Oct-31-11	Nov-16...	200d

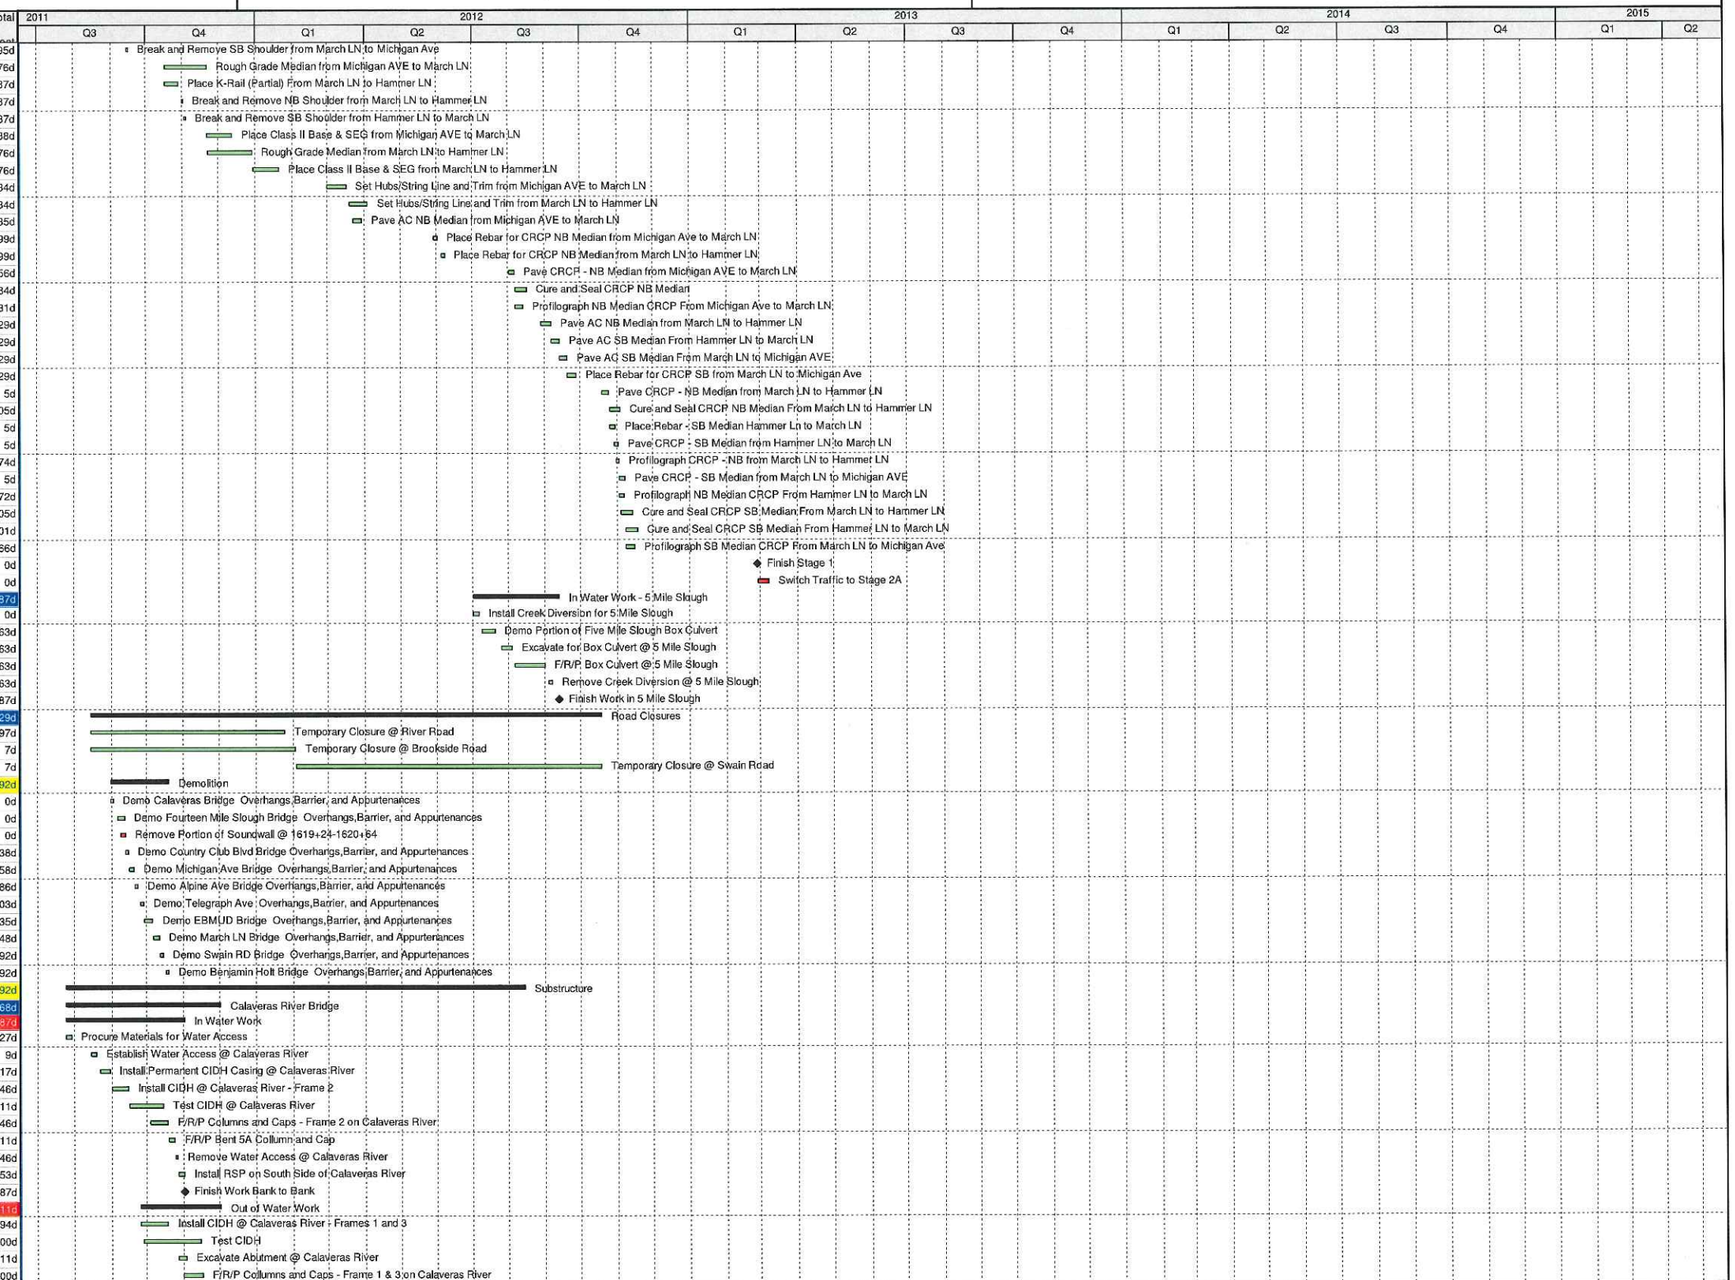

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Start Date: Jun-16-11

Activity ID	Bid Item	211080 - Group	Activity Name	OD	Start	Finish	Total Float
A20		COOP	Install Concrete Pile @ ...	8d	Nov-03-11	Nov-15...	211d
A19	141	RLB	F/R/P Abutments @ Cal...	10d	Nov-16-11	Dec-01...	211d
Fourteen Mile Slough				250d	Aug-15-11	Aug-14-...	29d
In Water Work				54d	Aug-15-11	Oct-31-11	0d
A15		RLB	Establish Water Access...	5d	Aug-15-11	Aug-19-...	9d
A23		CASE	Install Permanent CIDH ...	10d	Aug-22-11	Sep-02...	9d
A15	127	CASE	Install CIDH @ 14 Mile ...	13d	Sep-07-11	Sep-23...	0d
A24		CT	Test CIDH @ 14 Mile Sl...	20d	Oct-05-11	Oct-25-11	0d
A15	141	RLB	F/R/P Columns @ 14 M...	10d	Oct-12-11	Oct-26-11	0d
A15		RLB	Remove Water Access ...	3d	Oct-26-11	Oct-31-11	0d
A70		RLB	Finsh Work Bank to Bank	0d		Oct-31-11	0d
Out of Water Work				204d	Oct-19-11	Aug-14-...	29d
A23	141	RLB	F/R/P Caps @ 14 Mile ...	10d	Oct-19-11	Nov-02...	223d
A17	81	RLB	Excavate Abutment Foo...	10d	Oct-31-11	Jul-16-12	29d
A20	124	CASE	Install CIDH @ 14 Mile ...	6d	Jul-16-12	Jul-24-12	29d
A16	141	RLB	F/R/P Abutments @ 14 ...	15d	Jul-24-12	Aug-14-...	29d
Country Club BLVD				17d	Oct-31-11	Nov-28...	6d
A1960	81	RLB	Excavate for Abutments...	4d	Oct-31-11	Nov-04...	6d
A1710		COOP	Install Abutment Piling ...	3d	Nov-04-11	Nov-09...	6d
A1700	141	RLB	F/R/P Abutments @ C...	10d	Nov-09-11	Nov-28...	6d
Michigan Ave				17d	Oct-31-11	Nov-28...	28d
A1800	81	RLB	Excavate for Abutment ...	4d	Oct-31-11	Nov-04...	28d
A1790		COOP	Install Piling @ Abutmen...	3d	Nov-04-11	Nov-09...	28d
A1770	141	RLB	F/R/P Abutments @ Mi...	10d	Nov-09-11	Nov-28...	28d
Alpine Ave				23d	Nov-04-11	Dec-12...	49d
A1810	81	RLB	Excavate for Abutment ...	4d	Nov-04-11	Nov-10...	55d
A1820		COOP	Install Piling @ Abutmen...	3d	Nov-10-11	Nov-16...	55d
A1830	141	RLB	F/R/P Abutments @ Alp...	10d	Nov-28-11	Dec-12...	49d
Telegraph Ave				23d	Nov-04-11	Dec-12...	69d
A1840	81	RLB	Excavate for Abutment ...	4d	Nov-04-11	Nov-10...	75d
A1850		COOP	Install Piling @ Abutmen...	3d	Nov-10-11	Nov-16...	75d
A1860	141	RLB	F/R/P Abutments @ Tel...	10d	Nov-28-11	Dec-12...	69d
EBMUD Aqueduct				145d	Oct-19-11	May-18...	5d
A1550	127	CASE	Install CIDH @ EBMUD...	10d	Oct-19-11	Nov-01...	94d
A2620		CT	Test CIDH	34d	Oct-21-11	Dec-12...	94d
A1740	81	RLB	Excavate for Abutments...	5d	Nov-10-11	Nov-18...	106d
A1490	124	CASE	Install CIDH @ EBMUD...	7d	Dec-06-11	Dec-14...	97d
A1500	141	RLB	F/R/P Abutment @ EB...	15d	Dec-15-11	Jan-06-12	97d
A7860	141	RLB	F/R/P Collumns @ EB...	20d	Apr-23-12	May-18...	5d
March LN				29d	Nov-10-11	Dec-27...	112d
A1870	81	RLB	Excavate for Abutment ...	4d	Nov-10-11	Nov-17...	124d
A1880		COOP	Install Piling @ Abutmen...	3d	Nov-17-11	Nov-22...	124d
A1890	141	RLB	F/R/P Abutments @ Ma...	10d	Dec-12-11	Dec-27...	112d
Swain RD				67d	Oct-13-11	Jan-23-12	147d
A1900	81	RLB	Excavate for Abutment ...	4d	Oct-13-11	Oct-18-11	197d
A1910		COOP	Install Piling @ Abutmen...	3d	Oct-19-11	Oct-21-11	197d
A1920	141	RLB	F/R/P Abutments @ Sw...	10d	Jan-09-12	Jan-23-12	147d
Benjamin Holt DR				35d	Nov-17-11	Jan-11-12	154d
A1930	81	RLB	Excavate for Abutment ...	4d	Nov-17-11	Nov-23...	172d
A1940		COOP	Install Piling @ Abutmen...	3d	Nov-23-11	Nov-30...	172d
A1950	141	RLB	F/R/P Abutments @ Be...	10d	Dec-27-11	Jan-11-12	154d
Superstructure				280d	Nov-17-11	Jan-03-13	35d
Calaveras River Bridge - CIP T-Beam & PC I-Beam				260d	Nov-17-11	Dec-04...	41d
A2870		RLB	14 Day Waiting Period	14d	Nov-17-11	Dec-08...	206d
A2590		RLB	Set Falsework for Calve...	10d	Dec-05-11	Dec-16...	200d
A2320	141	RLB	F/R/P Soffit & Stem @ ...	15d	Dec-19-11	Jan-10-12	200d
A1990	141	RLB	F/R/P Deck @ Calavera...	7d	Jan-12-12	Jan-24-12	206d
A8140	141	RLB	F/R/P Deck @ Calavera...	7d	Jan-24-12	Feb-02-...	206d
A2690		RLB	10 Day Waiting Period	10d	Feb-02-12	Feb-17-...	216d
A7920		RLB	60 Day Waiting Period	60d	Feb-03-12	Apr-02-12	301d
A2330		CONF	Place Precast Girders &...	5d	Feb-17-12	Feb-27-...	216d
A8150	141	RLB	F/R/P Deck @ Calavera...	4d	Feb-27-12	Mar-02-...	216d
A2800		RLB	Hinge 1 and 2 Retrofit	10d	Mar-02-12	Mar-16-...	216d
A2050	141	RLB	Closure Pour @ Calave...	5d	Apr-02-12	Apr-09-12	205d
A2020		RLB	Construct Approaches ...	4d	Nov-29-12	Dec-04...	35d
Fourteen Mile Slough - PC/PS Deck Units				87d	Aug-14-12	Dec-20...	35d
A7060		CONF	Set Precast Deck Units	10d	Aug-14-12	Aug-28-...	29d
A6960	141	RLB	Closure Pour @ Fourte...	5d	Aug-28-12	Sep-05...	103d
A3480		RLB	Construct Approaches ...	4d	Dec-17-12	Dec-20...	35d
Country Club BLVD - Box Girder				137d	Nov-28-11	Jun-14-12	161d
A2980		RLB	Set Falsework @ Count...	10d	Nov-28-11	Dec-12...	6d
A2960	141	RLB	F/R/P Stem & Soffit @ ...	25d	Dec-12-11	Jan-19-12	6d
A2970	141	RLB	F/R/P Deck @ Country ...	10d	Jan-19-12	Feb-02-...	6d
A3080		RLB	10 Day Waiting Period f...	10d	Feb-03-12	Feb-12-...	9d

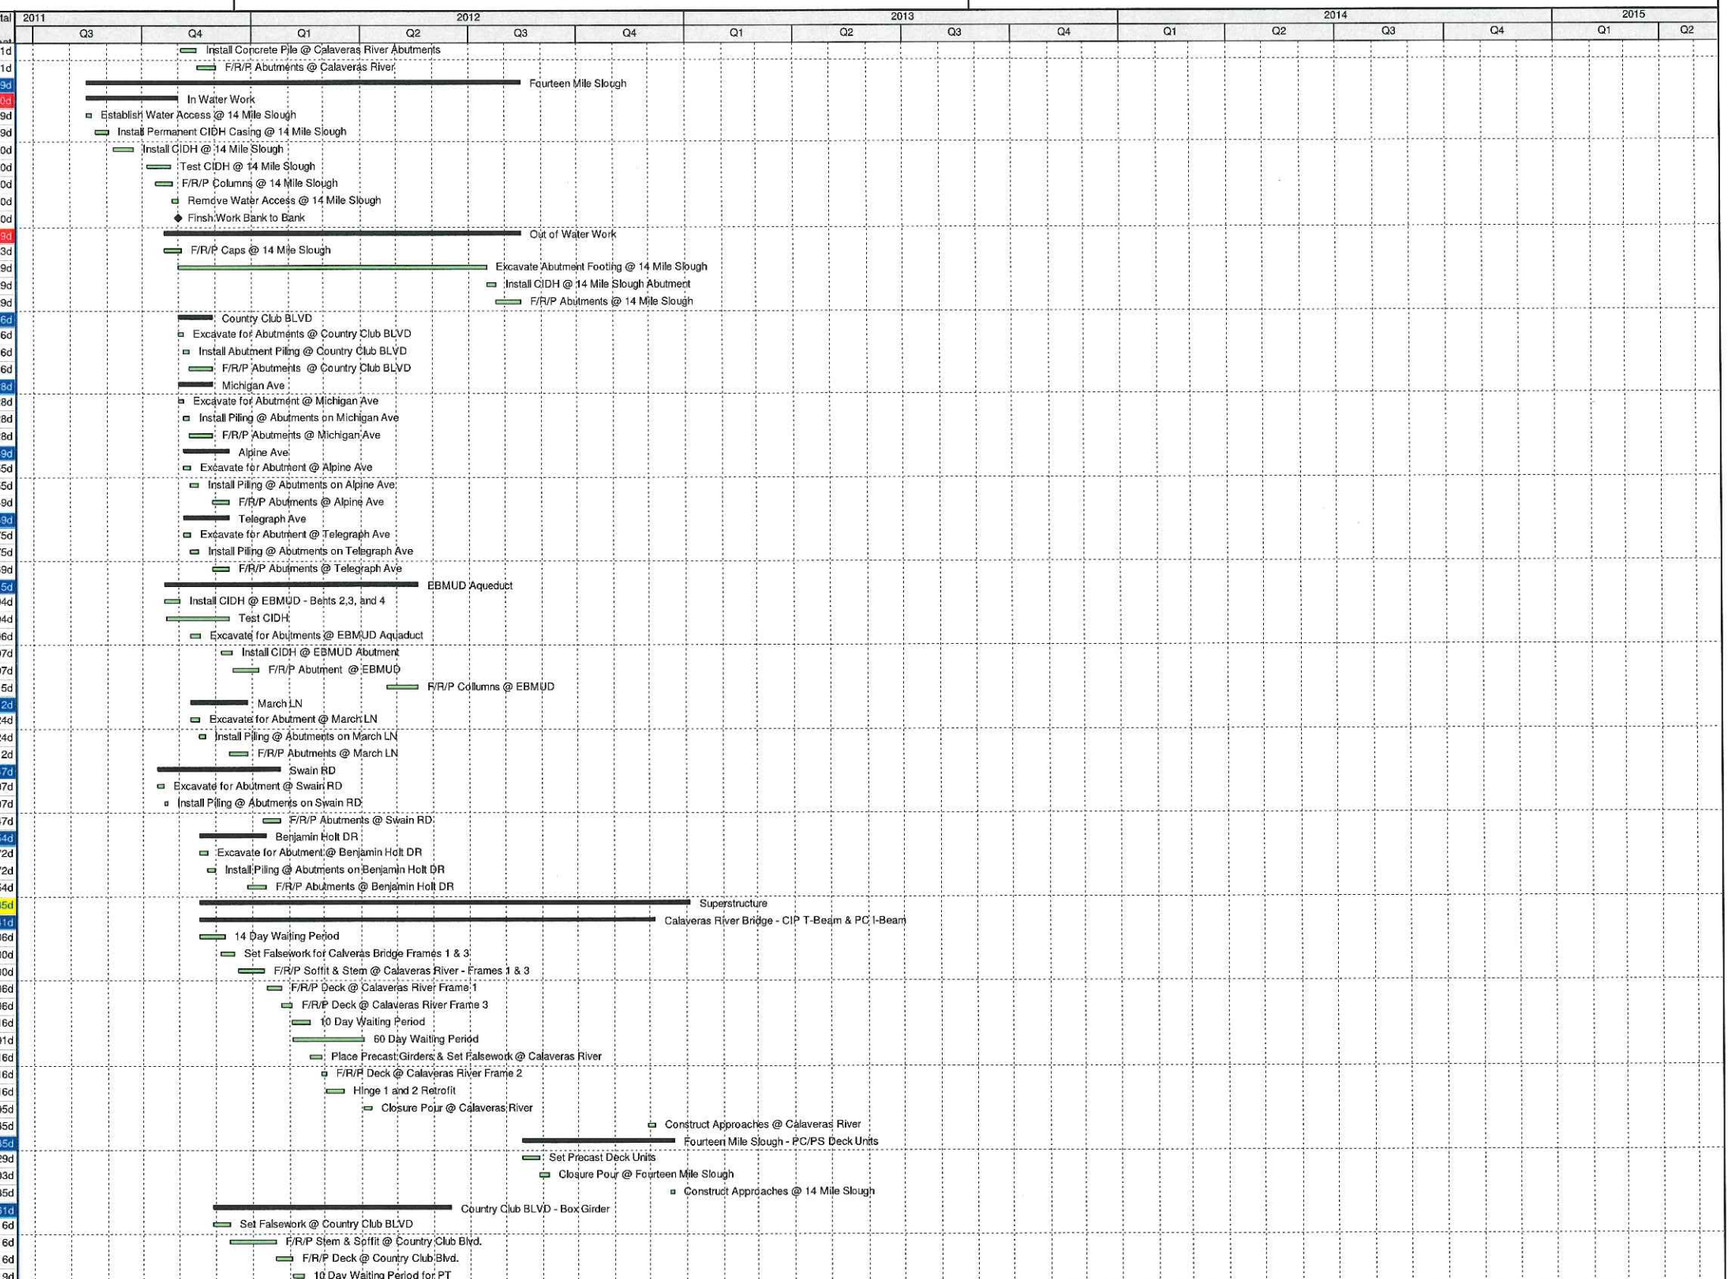

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Start Date: Jun-16-11
