Activity ID	Bid Item	211080 - Group	Activity Name	OD	Start	Finish	Total Float
A3060		RLB	60 Day Waiting Period f...	60d	Feb-13-12	Apr-12-12	298d
A2990	138	AVAR	Post Tension @ Countr...	3d	Feb-14-12	Feb-16-...	5d
A6970	141	RLB	Closure Pour @ Countr...	3d	Apr-12-12	Apr-17-12	202d
A3420		RLB	Construct Approaches ...	4d	Jun-11-12	Jun-14-12	136d
Michigan Ave - Box Girder				242d	Nov-28-11	Nov-14...	56d
A3020		RLB	Set Falsework @ Michi...	10d	Nov-28-11	Dec-12-...	28d
A3000	141	RLB	F/R/P Stem & Soffit @ ...	25d	Dec-12-11	Jan-19-12	28d
A3010	141	RLB	F/R/P Deck @ Michigan...	10d	Jan-19-12	Feb-02-...	28d
A8000		RLB	10 Day Waiting Period f...	10d	Feb-03-12	Feb-12-...	42d
A7930		RLB	60 Day Waiting Period	60d	Feb-13-12	Apr-12-12	298d
A3030	138	AVAR	Post Tension @ Michig...	3d	Feb-17-12	Feb-22-...	175d
A6980	141	RLB	Closure Pour @ Michig...	3d	May-22-12	May-24-...	175d
A3430		RLB	Construct Approaches ...	4d	Nov-08-12	Nov-14-...	35d
Alpine Ave - Box Girder				192d	Feb-17-12	Nov-20...	55d
A7800		RLB	Set Falsework @ Alpine...	10d	Feb-17-12	Mar-02-...	5d
A3040	141	RLB	F/R/P Stem & Soffit @ ...	25d	Mar-05-12	Apr-06-12	5d
A3050	141	RLB	F/R/P Deck @ Alpine Ave	10d	Apr-09-12	Apr-20-12	5d
A8010		RLB	10 Day Waiting Period f...	10d	Apr-21-12	Apr-30-12	28d
A3070	138	AVAR	Post Tension @ Alpine ...	3d	Apr-30-12	May-03...	169d
A7940		RLB	60 Day Waiting Period	60d	May-01-12	Jun-29-12	223d
A6990	141	RLB	Closure Pour @ Alpine ...	3d	Jun-29-12	Jul-05-12	150d
A3440		RLB	Construct Approaches ...	4d	Nov-15-12	Nov-20...	35d
Telegraph Ave - Box Girder				199d	Feb-14-12	Nov-28...	53d
A7810		RLB	Set Falsework @ Telegr...	10d	Feb-14-12	Feb-28-...	28d
A3090	141	RLB	F/R/P Stem & Soffit @ ...	25d	Feb-29-12	Apr-03-12	28d
A3100	141	RLB	F/R/P Deck @ Telegrap...	10d	Apr-04-12	Apr-17-12	28d
A8020		RLB	10 Day Waiting Period f...	10d	Apr-18-12	Apr-27-12	41d
A3120	138	AVAR	Post Tension @ Telegr...	3d	Apr-27-12	May-02...	174d
A7950		RLB	60 Day Waiting Period	60d	Apr-28-12	Jun-26-12	231d
A7000	141	RLB	Closure Pour @ Telegr...	3d	Jun-26-12	Jun-29-12	155d
A3450		RLB	Construct Approaches ...	4d	Nov-21-12	Nov-28...	35d
EBMUD Aqueduct - Box Girder				139d	May-21-12	Dec-10...	48d
A7820		RLB	Set Falsework @ EBM...	15d	May-21-12	Jun-11-12	5d
A3140	141	RLB	F/R/P Stem & Soffit @ ...	25d	Jun-12-12	Jul-17-12	5d
A3150	141	RLB	F/R/P Deck @ EBMUD ...	10d	Jul-18-12	Jul-31-12	5d
A7960		RLB	60 Day Waiting Period	60d	Aug-01-12	Sep-29...	137d
A7150		RLB	10 Day Waiting Period t...	10d	Aug-01-12	Aug-14-...	5d
A7010	141	RLB	Closure Pour @ EBMUD	5d	Oct-01-12	Oct-05-12	90d
A3460		RLB	Construct Approaches ...	4d	Dec-05-12	Dec-10...	35d
March LN - Box Girder				158d	Apr-27-12	Dec-14...	44d
A7830		RLB	Set Falsework @ March...	10d	Apr-27-12	May-11...	28d
A3190	141	RLB	F/R/P Stem & Soffit @ ...	25d	May-11-12	Jun-18-12	28d
A3200	141	RLB	F/R/P Deck @ March LN	10d	Jun-18-12	Jul-02-12	28d
A8040		RLB	10 Day Waiting Period f...	10d	Jul-03-12	Jul-12-12	40d
A3220	138	AVAR	Post Tension @ March ...	3d	Jul-12-12	Jul-17-12	134d
A7970		RLB	60 Day Waiting Period	60d	Jul-13-12	Sep-10...	161d
A7020	141	RLB	Closure Pour @ March LN	3d	Sep-10-12	Sep-13...	106d
A3470		RLB	Construct Approaches ...	4d	Dec-11-12	Dec-14...	35d
Swain RD - Box Girder				117d	Jul-12-12	Jan-02-13	36d
A7840		RLB	Set Falsework @ Swain...	10d	Jul-12-12	Jul-26-12	28d
A3230	141	RLB	F/R/P Stem & Soffit @ ...	25d	Jul-26-12	Aug-30-...	28d
A3240	141	RLB	F/R/P Deck @ Swain RD	10d	Oct-03-12	Oct-18-12	5d
A8050		RLB	10 Day Waiting Period f...	10d	Oct-19-12	Oct-28-12	56d
A3260	138	AVAR	Post Tension @ Swain ...	3d	Oct-29-12	Oct-31-12	68d
A7980		RLB	60 Day Waiting Period	60d	Oct-29-12	Dec-27...	56d
A3490		RLB	Construct Approaches ...	4d	Dec-21-12	Dec-27...	35d
A7030	141	RLB	Closure Pour @ Swain Rd	3d	Dec-27-12	Jan-02-13	36d
Benjamin Holt DR - Box Girder				95d	Aug-15-12	Jan-03-13	35d
A7850		RLB	Set Falsework @ Benja...	10d	Aug-15-12	Aug-28-...	5d
A3280	141	RLB	F/R/P Stem and Soffit ...	25d	Aug-29-12	Oct-03-12	5d
A3290	141	RLB	F/R/P Deck @ Benjami...	10d	Oct-04-12	Oct-18-12	5d
A8060		RLB	10 Day Waiting Period f...	10d	Oct-19-12	Oct-28-12	56d
A7990		RLB	60 Day Waiting Period	60d	Oct-29-12	Dec-27...	56d
A3310	138	AVAR	Post Tension @ Benja...	3d	Nov-01-12	Nov-05...	69d
A7040	141	RLB	Closure Pour@ Benjami...	3d	Dec-27-12	Jan-02-13	36d
A3500		RLB	Construct Approaches ...	4d	Dec-28-12	Jan-03-13	35d
Walls				359d	Sep-14-11	Feb-26-...	74d
Soundwall "M"				44d	Sep-14-11	Nov-16...	194d
A2070	84	RLB	Excavate Foundation - ...	5d	Sep-14-11	Sep-20...	0d
A2350	137	CASE	Install 16" CIDH - SW "M"	1d	Sep-21-11	Sep-21...	0d
A2470	142	RLB	F/R/P Foundation SW "M"	10d	Sep-22-11	Oct-05-11	0d
A2490	142	RLB	F/R/P Wall SW "M"	14d	Oct-06-11	Oct-26-11	0d
A2540		RLB	F/R/P Barrier SW "M"	14d	Oct-27-11	Nov-16...	194d

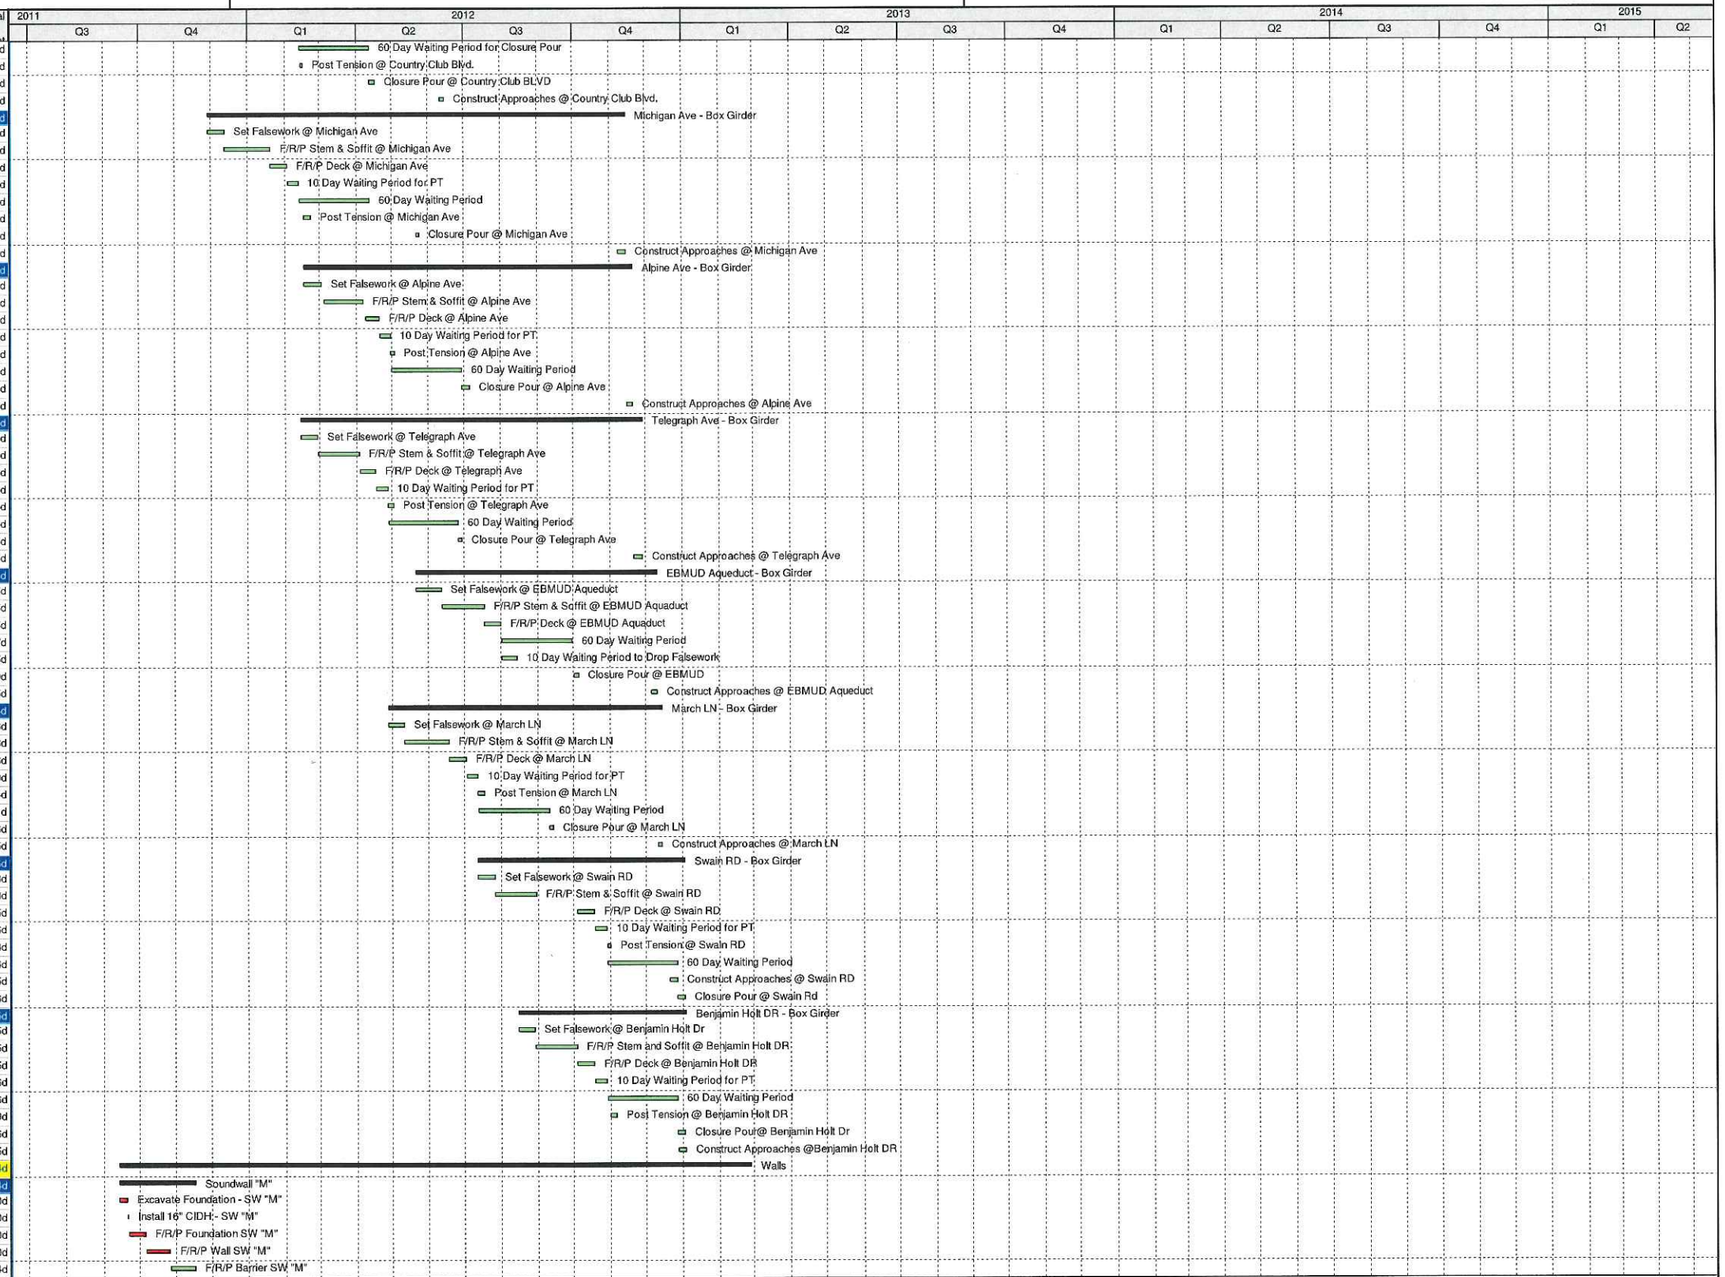

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Start Date: Jun-16-11

Activity ID	Bid Item	211080 - Group	Activity Name	OD	Start	Finish	Total Float
Crib Wall				32d	Oct-27-11	Dec-14...	0d
A1340	83	RLB	Excavate - Crib Wall Su...	8d	Oct-27-11	Nov-07...	0d
A2550		RLB	Fine Grade	5d	Nov-08-11	Nov-15...	0d
A1350	159	RLB	Construct Crib Wall	19d	Nov-16-11	Dec-14...	0d
Basin Wall No. 2				34d	Dec-15-11	Feb-03-...	5d
A2110	84	RLB	Excavate Foundation - ...	5d	Dec-15-11	Dec-21...	0d
A2560	142	RLB	F/R/P Foundation - BW ...	14d	Dec-22-11	Jan-12-12	0d
A2580	142	RLB	F/R/P Wall - BW No. 2	15d	Jan-13-12	Feb-03-...	5d
Basin Wall No. 4				35d	Jan-13-12	Mar-06-...	0d
A2140	84	RLB	Excavate Foundation - ...	5d	Jan-13-12	Jan-20-12	0d
A2150	142	RLB	F/R/P BW No. 4 Found...	15d	Jan-23-12	Feb-10-...	0d
A2160	142	RLB	F/R/P BW No. 4	15d	Feb-14-12	Mar-06-...	0d
Basin Wall No. 5				39d	Feb-14-12	Apr-09-12	0d
A2170	84	RLB	Excavate Foundation - ...	10d	Feb-14-12	Feb-28-...	5d
A2180	142	RLB	F/R/P BW No. 5 Found...	10d	Mar-07-12	Mar-20-...	0d
A2190	142	RLB	F/R/P BW No. 5	14d	Mar-21-12	Apr-09-12	0d
Basin Wall No. 6				39d	Mar-21-12	May-14...	15d
A2240	84	RLB	Excavate Foundation - ...	10d	Mar-21-12	Apr-03-12	4d
A2250	142	RLB	F/R/P BW No. 6 Found...	15d	Apr-10-12	Apr-30-12	0d
A2260	142	RLB	F/R/P BW No. 6	10d	May-01-12	May-14...	15d
Basin Wall No. 7				35d	May-01-12	Jun-19-12	0d
A2270	84	RLB	Excavate Foundation - ...	10d	May-01-12	May-14...	0d
A2280	142	RLB	F/R/P BW No. 7 Found...	15d	May-15-12	Jun-05-12	0d
A2290	142	RLB	F/R/P BW No. 7	10d	Jun-06-12	Jun-19-12	0d
Basin Wall No. 10				30d	Jun-06-12	Jul-18-12	149d
A2930	84	RLB	Excavate Foundation - ...	8d	Jun-06-12	Jun-15-12	2d
A2940	142	RLB	F/R/P BW No. 10 Foun...	10d	Jun-20-12	Jul-03-12	0d
A2950	142	RLB	F/R/P BW No. 10	10d	Jul-05-12	Jul-18-12	149d
Sound Wall No. 2				43d	Jul-05-12	Sep-04...	5d
A1370	84	RLB	Excavate Pile Cap Foun...	8d	Jul-05-12	Jul-16-12	0d
A2080	137	CASE	Install 16" CIDH -SW N...	10d	Jul-17-12	Jul-30-12	0d
A1460	142	RLB	F/R/P Pile Cap Foundat...	15d	Jul-31-12	Aug-20-...	0d
A2130		RLB	F/R/P Barrier - SW No. 2	10d	Aug-21-12	Sep-04...	5d
Sound Wall No. 4				75d	Aug-21-12	Dec-10...	125d
A2200	84	RLB	Excavate Foundation - ...	15d	Aug-21-12	Sep-11...	0d
A2210	142	RLB	F/R/P Foundation - SW...	15d	Sep-12-12	Oct-02-12	0d
A7160	142	RLB	F/R/P Wall - SW No. 4	25d	Oct-03-12	Nov-07...	21d
A2220		RLB	F/R/P Barrier - SW No. 4	20d	Nov-08-12	Dec-10...	125d
Sound Wall No. 4a				40d	Oct-03-12	Dec-03...	21d
A2810	84	RLB	Excavate Pile Cap Foun...	7d	Oct-03-12	Oct-12-12	0d
A2390	137	CASE	Install 16" CIDH -SW N...	1d	Oct-15-12	Oct-15-12	0d
A2820	142	RLB	F/R/P Pile Cap Foundat...	7d	Oct-16-12	Oct-24-12	0d
A2830		RLB	F/R/P Barrier - SW No. 4a	15d	Nov-08-12	Dec-03...	21d
Sound Wall No. 6				50d	Oct-25-12	Jan-09-13	16d
A2840	84	RLB	Excavate Pile Cap Foun...	10d	Oct-25-12	Nov-07...	0d
A2400	137	CASE	Install 16" CIDH -SW N...	10d	Nov-08-12	Nov-26...	0d
A2850	142	RLB	F/R/P Pile Cap Foundat...	10d	Nov-27-12	Dec-10...	0d
A2860		RLB	F/R/P Barrier - SW No. 6	20d	Dec-11-12	Jan-09-13	16d
Sound Wall No. 6a				51d	Dec-11-12	Feb-26-...	0d
A2900	84	RLB	Excavate Pile Cap Foun...	6d	Dec-11-12	Dec-18...	0d
A2410	137	CASE	Install 16" CIDH -SW N...	2d	Dec-19-12	Dec-20...	0d
A2910	142	RLB	F/R/P Pile Cap Foundat...	8d	Dec-21-12	Jan-03-13	0d
A7130	142	RLB	F/R/P Wall - SW No. 6a	20d	Jan-04-13	Feb-01-...	0d
A2920		RLB	F/R/P Barrier - SW No. 6a	15d	Feb-04-13	Feb-26-...	0d
Stage 2A				117d	Mar-08-13	Aug-22-...	0d
Roadwork				117d	Mar-08-13	Aug-22-...	0d
A4950		SWPP	Install Stage 2A BMP's	5d	Mar-08-13	Mar-14-...	0d
A5030	4	RLB	Install Stage 2A ESA Fe...	5d	Mar-08-13	Mar-14-...	0d
A4220	76	ROCK	Break and Remove PC...	6d	Mar-15-13	Mar-22-...	0d
A4240		RLB	Rough Grade From Sta ...	14d	Mar-25-13	Apr-12-13	0d
A4300	76	ROCK	Break and Remove PC...	6d	Mar-25-13	Apr-02-13	8d
A4380	76	ROCK	Break and Remove PC...	4d	Apr-03-13	Apr-08-13	10d
A4450	76	RLB	Strip Existing Asphalt Fr...	4d	Apr-09-13	Apr-12-13	10d
A4320		RLB	Rough Grade From Sta ...	6d	Apr-15-13	Apr-22-13	0d
A4460	76	ROCK	Break and Remove PC...	8d	Apr-15-13	Apr-24-13	10d
A4530		RLB	Strip Existing Asphalt Fr...	3d	Apr-15-13	Apr-17-13	24d
A4290		RLB	Install Underground Utilit...	2d	Apr-15-13	Apr-16-13	21d
A4250	101	RLB	Place Class II Base and...	8d	Apr-17-13	Apr-26-13	21d
A4400		RLB	Rough Grade From Sta ...	12d	Apr-23-13	May-08...	0d
A7190		RLB	Install Underground Utilit...	2d	Apr-23-13	Apr-24-13	33d
A4330	101	RLB	Place Class II Base and...	3d	Apr-25-13	Apr-29-13	33d
A4540	76	ROCK	Break and Remove PC...	6d	Apr-25-13	May-02...	19d
A4260		RLB	Set Hubs/String Line an...	7d	Apr-29-13	May-07...	21d

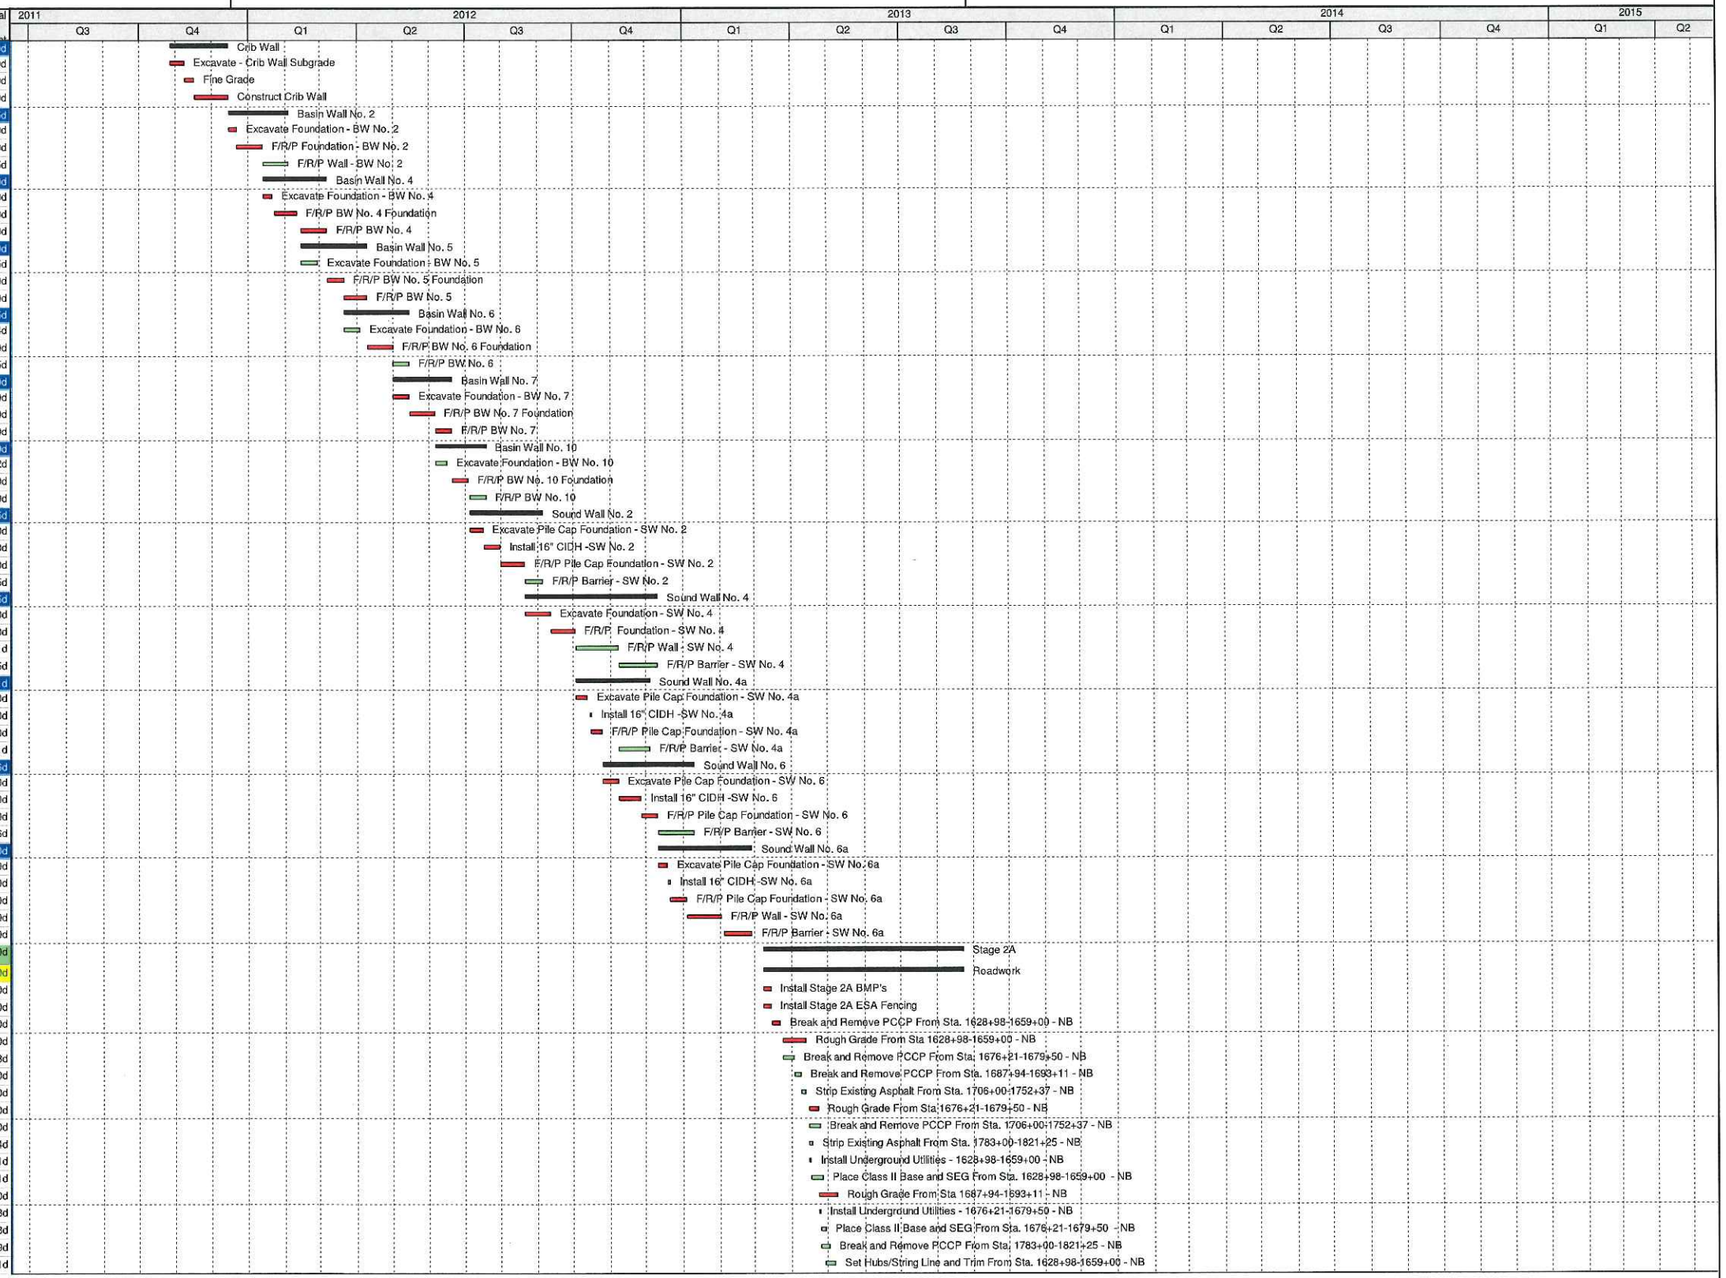

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Start Date: Jun-16-11

Activity ID	Bid Item	211080 - Group	Activity Name	OD	Start	Finish	Total Float
A4340		RLB	Set Hubs/String Line an...	2d	May-08-13	May-09...	27d
A4310	104	OCJI	Pave AC From Sta. 162...	2d	May-08-13	May-09...	21d
A4480		RLB	Rough Grade From Sta ...	15d	May-09-13	May-30...	0d
A7200		RLB	Install Underground Utilit...	3d	May-09-13	May-13...	21d
A4270	112	CMCF	Place Rebar From Sta. ...	6d	May-10-13	May-17...	21d
A4370	104	OCJI	Pave AC From Sta. 167...	2d	May-10-13	May-13...	30d
A4410	101	RLB	Place Class II Base and...	4d	May-14-13	May-17...	21d
A4280	112	RLB	Pave CRCP From Sta. ...	6d	May-20-13	May-28...	21d
A4350	112	CMCF	Place Rebar From Sta. ...	2d	May-20-13	May-21...	27d
A4420		RLB	Set Hubs/String Line an...	3d	May-20-13	May-22...	21d
A4360	112	RLB	Pave CRCP From Sta. ...	2d	May-22-13	May-23...	35d
A4390	104	OCJI	Pave AC From Sta. 168...	2d	May-23-13	May-24...	23d
A4430	112	CMCF	Place Rebar From Sta....	3d	May-28-13	May-30...	24d
A4230		RLB	Profilograph CRCP Fro...	2d	May-29-13	May-30...	44d
A5130	119	RLB	Pave JPCP From Sta. ...	3d	May-29-13	May-31...	38d
A4440	112	RLB	Pave CRCP From Sta. ...	4d	May-31-13	Jun-05-13	24d
A4560		RLB	Rough Grade From Sta ...	14d	May-31-13	Jun-19-13	0d
A7210		RLB	Install Underground Utilit...	5d	May-31-13	Jun-06-13	4d
A4630		RLB	Profilograph CRCP Fro...	1d	May-31-13	May-31...	44d
A5180	119	RLB	Pave JPCP From Sta. ...	2d	Jun-03-13	Jun-04-13	38d
A4710		RLB	Profilograph CRCP Fro...	1d	Jun-06-13	Jun-06-13	41d
A5240	119	RLB	Pave JPCP From Sta. ...	3d	Jun-06-13	Jun-10-13	37d
A4490	101	RLB	Place Class II Base and...	7d	Jun-07-13	Jun-17-13	4d
A4500		RLB	Set Hubs/String Line an...	4d	Jun-18-13	Jun-21-13	4d
A7220		RLB	Install Underground Utilit...	5d	Jun-20-13	Jun-26-13	0d
A4470	104	OCJI	Pave AC From Sta. 170...	4d	Jun-24-13	Jun-27-13	4d
A4570	101	RLB	Place Class II Base and...	10d	Jun-27-13	Jul-11-13	0d
A4510	112	CMCF	Place Rebar From Sta. ...	4d	Jun-28-13	Jul-03-13	4d
A4520	112	RLB	Pave CRCP From Sta. ...	5d	Jul-05-13	Jul-11-13	4d
A4580		RLB	Set Hubs/String Line an...	5d	Jul-12-13	Jul-18-13	0d
A4790		RLB	Profilograph CRCP Fro...	2d	Jul-12-13	Jul-15-13	17d
A5470	119	RLB	Pave JPCP From Sta. ...	3d	Jul-12-13	Jul-16-13	15d
A4550	104	OCJI	Pave AC From Sta. 178...	3d	Jul-19-13	Jul-23-13	0d
A4590	112	CMCF	Place Rebar From Sta. ...	5d	Jul-24-13	Jul-30-13	0d
A4600	112	RLB	Pave CRCP From Sta. ...	5d	Jul-31-13	Aug-06-...	0d
A4870		RLB	Profilograph CRCP Fro...	2d	Aug-07-13	Aug-08-...	1d
A5490	119	RLB	Pave JPCP From Sta. ...	3d	Aug-07-13	Aug-09-...	0d
A4170		RLB	Finish Stage 2A	0d		Aug-09-...	0d
A4180		CRSP	Switch Traffic to Stage 2B	7d	Aug-14-13	Aug-22-...	0d
Superstructure				50d	May-24-13	Aug-05-...	4d
A3840		CMCF	Construct Approaches ...	5d	May-24-13	May-31...	35d
A3750		CMCF	Construct Approaches ...	5d	May-29-13	Jun-04-13	21d
A3990		ACCW	Place Polyester Concre...	2d	Jun-05-13	Jun-06-13	27d
A3820		CMCF	Construct Approaches ...	5d	Jun-05-13	Jun-11-13	21d
A3850		CMCF	Construct Approaches ...	5d	Jun-06-13	Jun-12-13	27d
A4000		ACCW	Place Polyester Concre...	2d	Jun-12-13	Jun-13-13	24d
A3830		CMCF	Construct Approaches ...	5d	Jun-12-13	Jun-18-13	21d
A3860		CMCF	Construct Approaches ...	5d	Jun-13-13	Jun-19-13	27d
A4010		ACCW	Place Polyester Concre...	2d	Jun-19-13	Jun-20-13	21d
A4020		ACCW	Place Polyester Concre...	3d	Jun-21-13	Jun-25-13	21d
A4030		ACCW	Place Polyester Concre...	2d	Jun-26-13	Jun-27-13	21d
A4040		ACCW	Place Polyester Concre...	2d	Jun-28-13	Jul-01-13	21d
A3870		CMCF	Construct Approaches ...	5d	Jul-12-13	Jul-18-13	4d
A4050		ACCW	Place Polyester Concre...	3d	Jul-19-13	Jul-23-13	9d
A3880		CMCF	Construct Approaches ...	5d	Jul-19-13	Jul-25-13	4d
A4060		ACCW	Place Polyester Concre...	2d	Jul-26-13	Jul-29-13	7d
A3890		CMCF	Construct Approaches ...	5d	Jul-26-13	Aug-01-...	4d
A4070		ACCW	Place Polyester Concre...	2d	Aug-02-13	Aug-05-...	4d
Walls				65d	Mar-08-13	Jun-10-13	43d
A3620	170	JJMM	Place Masonry Block - ...	5d	Mar-08-13	Mar-14-...	43d
A3520	170	JJMM	Place Masonry Block - ...	10d	Mar-15-13	Mar-28-...	43d
A3540	170	JJMM	Place Masonry Block - ...	20d	Mar-29-13	Apr-26-13	43d
A3560	170	JJMM	Place Masonry Block - ...	5d	Apr-29-13	May-03...	43d
A3580	170	JJMM	Place Masonry Block - ...	20d	May-06-13	Jun-03-13	43d
A3600	170	JJMM	Place Masonry Block - ...	5d	Jun-04-13	Jun-10-13	43d
Stage 2B				244d	Aug-12-13	Aug-05-...	18d
Roadwork				164d	Aug-12-13	Apr-11-14	14d
A4200		OCJI	Remove STBB & Place...	2d	Aug-12-13	Aug-13-...	0d
A5010		SWPP	Install Stage 2B BMP's	5d	Aug-23-13	Aug-29-...	113d
A5050	4	RLB	Install Stage 2B ESA Fe...	5d	Aug-23-13	Aug-29-...	107d
A4620	76	ROCK	Break and Remove PC...	4d	Aug-30-13	Sep-05...	107d
A4770	76	RLB	Strip Existing Asphalt Fr...	2d	Aug-30-13	Sep-03...	113d

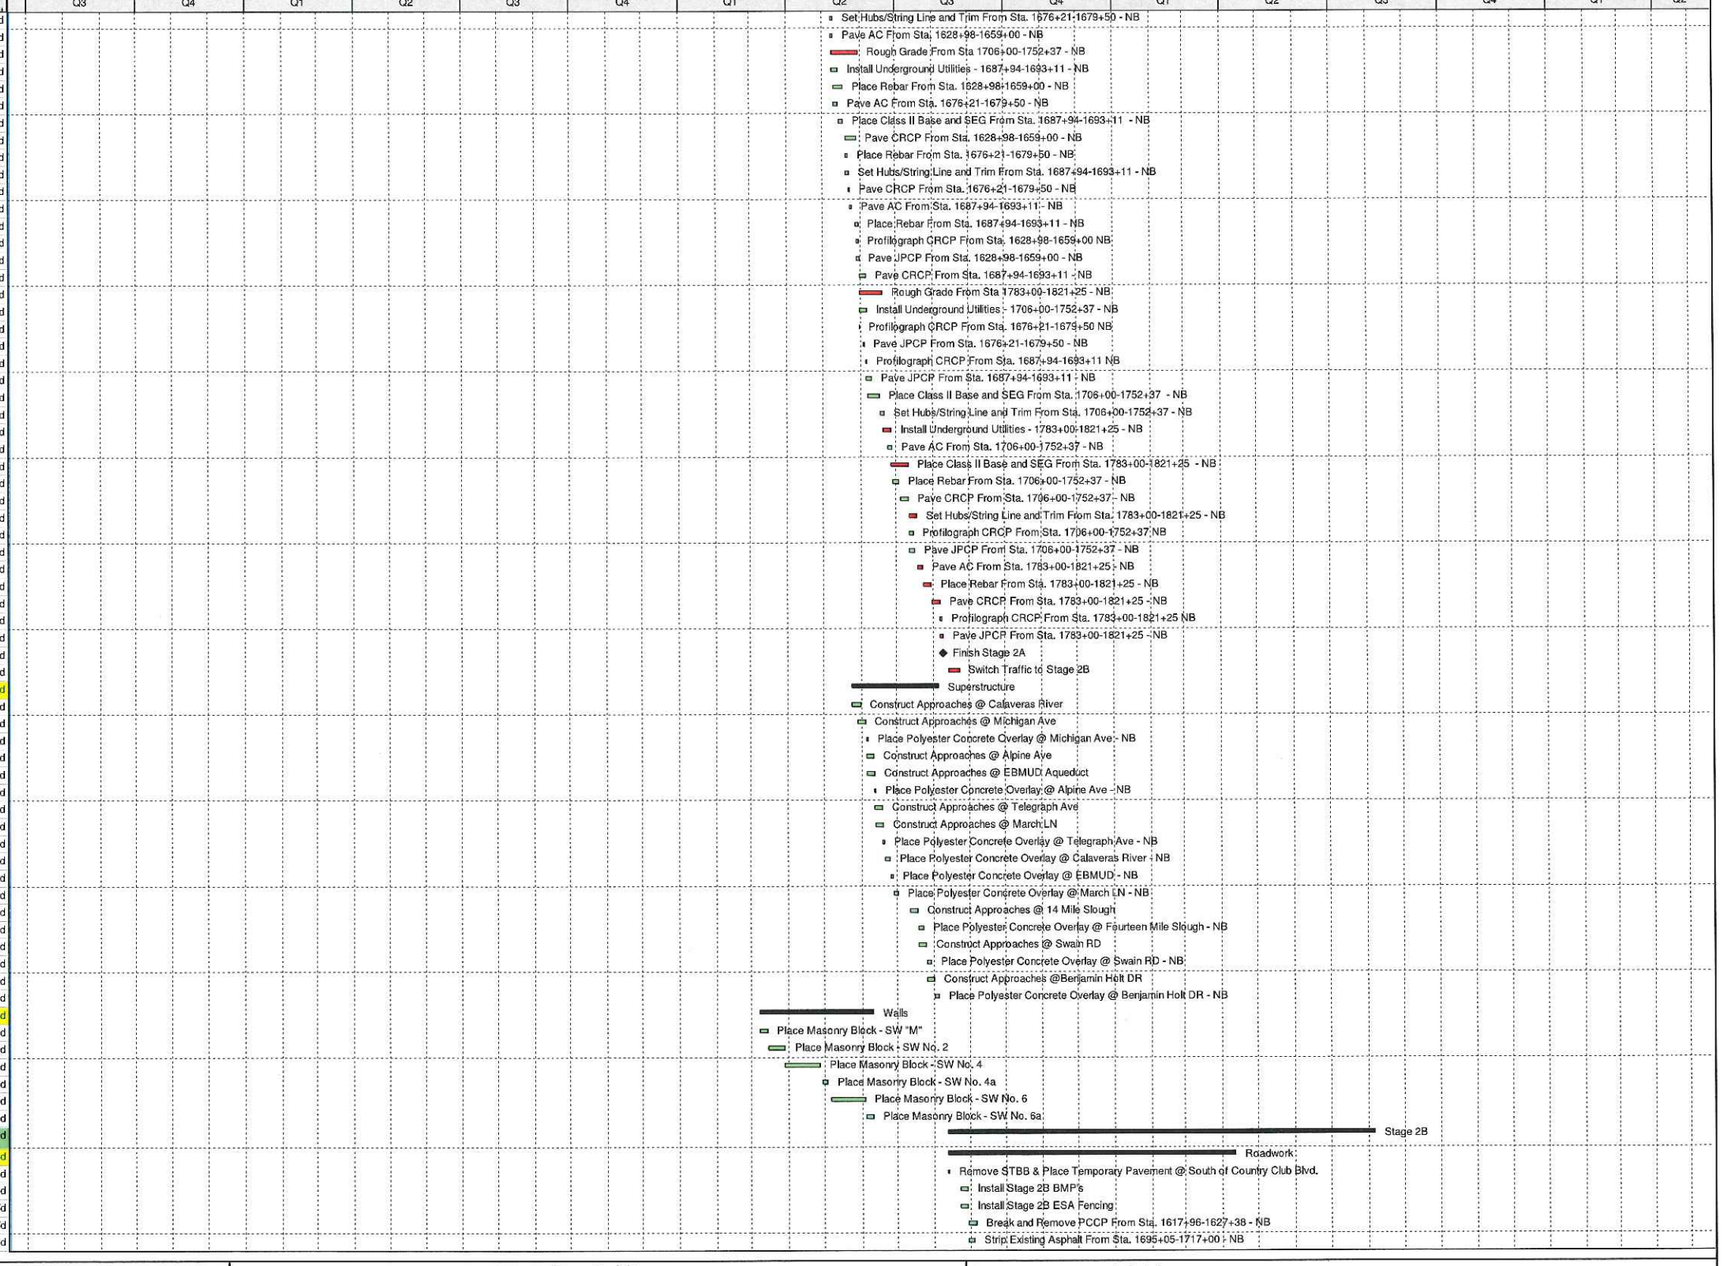

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Start Date: Jun-16-11
