Activity ID	Bid Item	211080 - Group	Activity Name	OD	Start	Finish	Total Float
A4850	76	RLB	Strip Existing Asphalt Fr...	3d	Sep-04-13	Sep-06...	113d
A4640		RLB	Rough Grade From Sta ...	2d	Sep-06-13	Sep-09...	110d
A4700	76	ROCK	Break and Remove PC...	6d	Sep-06-13	Sep-13...	107d
A4860	76	ROCK	Break and Remove PC...	6d	Sep-09-13	Sep-16...	113d
A4930	76	RLB	Strip Existing Asphalt Fr...	2d	Sep-09-13	Sep-10...	124d
A4210		RLB	Install Underground Utilit...	3d	Sep-10-13	Sep-12...	110d
A4650	101	RLB	Place Class II Base and...	3d	Sep-13-13	Sep-17...	118d
A4720		RLB	Rough Grade From Sta ...	2d	Sep-16-13	Sep-17...	107d
A4780	76	ROCK	Break and Remove PC...	4d	Sep-16-13	Sep-19...	107d
A4940	76	ROCK	Break and Remove PC...	4d	Sep-17-13	Sep-20...	120d
A4660		RLB	Set Hubs/String Line an...	2d	Sep-18-13	Sep-19...	50d
A7230		RLB	Install Underground Utilit...	4d	Sep-18-13	Sep-23...	107d
A4800		RLB	Rough Grade From Sta ...	2d	Sep-20-13	Sep-23...	107d
A7340	104	OCJI	Pave AC From Sta. 161...	2d	Sep-20-13	Sep-23...	118d
A4670	112	CMCF	Place Rebar From Sta. ...	3d	Sep-24-13	Sep-26...	50d
A4730	101	RLB	Place Class II Base and...	3d	Sep-24-13	Sep-26...	113d
A4880		RLB	Rough Grade From Sta ...	3d	Sep-24-13	Sep-26...	108d
A7240		RLB	Install Underground Utilit...	4d	Sep-24-13	Sep-27...	107d
A4680	112	RLB	Pave CRCP From Sta. ...	3d	Sep-27-13	Oct-01-13	50d
A4740		RLB	Set Hubs/String Line an...	2d	Sep-27-13	Sep-30...	45d
A4960		RLB	Rough Grade From Sta ...	2d	Sep-27-13	Sep-30...	116d
A4810	101	RLB	Place Class II Base and...	3d	Sep-30-13	Oct-02-13	109d
A7250		RLB	Install Underground Utilit...	5d	Sep-30-13	Oct-04-13	107d
A7350	104	OCJI	Pave AC From Sta. 165...	2d	Oct-01-13	Oct-02-13	114d
A7670		RLB	Profilograph CRCP Fro...	1d	Oct-02-13	Oct-02-13	130d
A8030	119	RLB	Pave JPCP From Sta. ...	3d	Oct-02-13	Oct-04-13	118d
A4750	112	CMCF	Place Rebar From Sta. ...	3d	Oct-03-13	Oct-07-13	46d
A4820		RLB	Set Hubs/String Line an...	2d	Oct-03-13	Oct-04-13	43d
A4890	101	RLB	Place Class II Base and...	4d	Oct-07-13	Oct-10-13	107d
A7260		RLB	Install Underground Utilit...	3d	Oct-07-13	Oct-09-13	112d
A7360	104	OCJI	Pave AC From Sta. 169...	3d	Oct-07-13	Oct-09-13	112d
A4760	112	RLB	Pave CRCP From Sta. ...	3d	Oct-08-13	Oct-10-13	46d
A4830	112	CMCF	Place Rebar From Sta. ...	3d	Oct-10-13	Oct-15-13	44d
A4900		RLB	Set Hubs/String Line an...	2d	Oct-11-13	Oct-15-13	39d
A4970	101	RLB	Place Class II Base and...	3d	Oct-11-13	Oct-16-13	111d
A7680		RLB	Profilograph CRCP Fro...	1d	Oct-11-13	Oct-11-13	124d
A8070	119	RLB	Pave JPCP From Sta. ...	4d	Oct-11-13	Oct-17-13	114d
A4840	112	RLB	Pave CRCP From Sta. ...	3d	Oct-16-13	Oct-18-13	44d
A7370	104	OCJI	Pave AC From Sta. 175...	4d	Oct-16-13	Oct-21-13	107d
A4980		RLB	Set Hubs/String Line an...	2d	Oct-17-13	Oct-18-13	43d
A7380	104	OCJI	Pave AC From Sta. 181...	2d	Oct-21-13	Oct-22-13	111d
A7690		RLB	Profilograph CRCP Fro...	1d	Oct-21-13	Oct-21-13	120d
A8080	119	RLB	Pave JPCP From Sta. ...	3d	Oct-21-13	Oct-23-13	113d
A4910	112	CMCF	Place Rebar From Sta. ...	4d	Oct-22-13	Oct-25-13	39d
A4920	112	RLB	Pave CRCP From Sta. ...	4d	Oct-28-13	Oct-31-13	39d
A4990	112	CMCF	Place Rebar From Sta. ...	3d	Oct-28-13	Oct-30-13	40d
A5000	112	RLB	Pave CRCP From Sta. ...	3d	Nov-01-13	Nov-05...	39d
A7700		RLB	Profilograph CRCP Fro...	1d	Nov-01-13	Nov-01...	112d
A8090	119	RLB	Pave JPCP From Sta. ...	4d	Nov-01-13	Nov-06...	107d
A8100	119	RLB	Pave JPCP From Sta. ...	3d	Nov-07-13	Nov-12...	107d
A7710		RLB	Profilograph CRCP Fro...	1d	Nov-12-13	Nov-12...	107d
A5080		RLB	Finish Stage 2B	0d		Apr-02-14	14d
A5090		CRSP	Switch Traffic to Stage 3A	7d	Apr-03-14	Apr-11-14	14d
Superstructure				6d	Oct-02-13	Oct-09-13	129d
A5020		CMCF	Construct Approaches ...	3d	Oct-02-13	Oct-04-13	129d
A5040		ACCW	Place Polyester Concre...	3d	Oct-07-13	Oct-09-13	129d
Walls				235d	Aug-23-13	Aug-05-...	18d
Basin Wall No. 11				28d	Aug-23-13	Oct-02-13	14d
A5420	84	RLB	Excavate Foundation - ...	8d	Aug-23-13	Sep-04...	14d
A5430	142	RLB	F/R/P BW No. 11 Foun...	10d	Sep-05-13	Sep-18...	14d
A5440	142	RLB	F/R/P BW No. 11	10d	Sep-19-13	Oct-02-13	14d
Basin Wall No. 9				35d	Sep-19-13	Nov-07...	14d
A5360	84	RLB	Excavate Foundation - ...	6d	Sep-19-13	Sep-26...	18d
A5370	142	RLB	F/R/P BW No. 9 Found...	15d	Oct-03-13	Oct-24-13	14d
A5380	142	RLB	F/R/P BW No. 9	10d	Oct-25-13	Nov-07...	14d
Basin Wall No. 8				45d	Oct-25-13	Jan-02-14	14d
A5260	84	RLB	Excavate Foundation - ...	8d	Oct-25-13	Nov-05...	16d
A5270	142	RLB	F/R/P BW No. 8 Found...	15d	Nov-08-13	Dec-03...	14d
A5250	142	RLB	F/R/P BW No. 8	20d	Dec-04-13	Jan-02-14	14d
Basin Wall No. 3				50d	Dec-04-13	Feb-18-...	14d
A5140	84	RLB	Excavate Foundation - ...	12d	Dec-04-13	Dec-19...	22d
A5150	142	RLB	F/R/P BW No. 3 Found...	10d	Jan-03-14	Jan-16-14	14d
A5160	142	RLB	F/R/P BW No. 3	20d	Jan-17-14	Feb-18-...	14d

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Start Date: Jun-16-11

Activity ID	Bid Item	211080 - Group	Activity Name	OD	Start	Finish	Total Float
Basin Wall No. 1				50d	Jan-17-14	Apr-02-14	14d
A5110	84	RLB	Excavate Foundation - ...	8d	Jan-17-14	Jan-29-14	26d
A5290	142	RLB	F/R/P Basin Wall Found...	10d	Feb-19-14	Mar-04-...	14d
A5120	142	RLB	F/R/P BW No. 1	20d	Mar-05-14	Apr-02-14	14d
Soundwall No. 7a				47d	Aug-23-13	Oct-30-13	15d
A5390	84	RLB	Excavate Foundation - ...	4d	Aug-23-13	Aug-28-...	0d
A2790	137	CASE	Install 16" CIDH -SW N...	1d	Aug-29-13	Aug-29-...	0d
A5400	142	RLB	F/R/P Foundation - SW...	12d	Aug-30-13	Sep-17...	0d
A5450	142	RLB	F/R/P Wall - SW No. 7a	10d	Sep-18-13	Oct-01-13	15d
A5410		RLB	F/R/P Barrier - SW No. 7a	20d	Oct-02-13	Oct-30-13	15d
Sound Wall No. 7				65d	Sep-18-13	Dec-23...	0d
A5330	84	RLB	Excavate Foundation - ...	10d	Sep-18-13	Oct-01-13	0d
A2730	142	RLB	F/R/P Foundation - SW ...	20d	Oct-02-13	Oct-30-13	0d
A7090	142	RLB	F/R/P Wall - SW No. 7	15d	Oct-31-13	Nov-21-...	0d
A5280		RLB	F/R/P Barrier - SW No. 7	20d	Nov-22-13	Dec-23-...	0d
Sound Wall No. 5a				74d	Nov-22-13	Mar-14-...	75d
A5300	84	RLB	Excavate Pile Cap Foun...	6d	Nov-22-13	Dec-03-...	2d
A2700	137	CASE	Install 16" CIDH -SW N...	12d	Dec-04-13	Dec-19-...	2d
A5310	142	RLB	F/R/P Foundation - SW ...	20d	Dec-24-13	Jan-23-14	0d
A7100	142	RLB	F/R/P Wall - SW No. 5a	14d	Jan-24-14	Feb-13-...	41d
A5320		RLB	F/R/P Barrier - SW No. 5a	20d	Feb-14-14	Mar-14-...	75d
Sound Wall No. 5				60d	Jan-24-14	Apr-22-14	64d
A5200	84	RLB	Excavate Foundation - ...	15d	Jan-24-14	Feb-14-...	0d
A5210	142	RLB	F/R/P Foundation - SW...	20d	Feb-18-14	Mar-17-...	0d
A7110	142	RLB	F/R/P Wall - SW No. 5	10d	Mar-18-14	Apr-01-14	20d
A5220		RLB	F/R/P Barrier - SW No. 5	15d	Apr-02-14	Apr-22-14	64d
Retaining Wall No. 1				55d	Mar-18-14	Jun-04-14	0d
A5230	84	RLB	Excavate Foundation -R...	15d	Mar-18-14	Apr-08-14	0d
A5340	142	RLB	F/R/P Foundation - RW ...	15d	Apr-09-14	Apr-29-14	0d
A5350	142	RLB	F/R/P RW No. 1	25d	Apr-30-14	Jun-04-14	0d
Sound Wall No. 3				56d	Apr-30-14	Jul-18-14	18d
A5170	84	RLB	Excavate Foundation - ...	8d	Apr-30-14	May-09-...	18d
A2640	142	RLB	F/R/P Foundation - SW ...	18d	May-12-14	Jun-05-14	18d
A7120	142	RLB	F/R/P Wall - SW No. 3	15d	Jun-06-14	Jun-26-14	18d
A5190		RLB	F/R/P Barrier - SW No. 3	15d	Jun-27-14	Jul-18-14	18d
Sound Wall No. 1				42d	Jun-06-14	Aug-05-...	18d
A5060	84	RLB	Excavate Pile Cap Foun...	6d	Jun-06-14	Jun-13-14	23d
A2610	137	CASE	Install 16" CIDH -SW N...	9d	Jun-16-14	Jun-26-14	23d
A5070	142	RLB	F/R/P Pile Cap Foundat...	10d	Jun-27-14	Jul-11-14	23d
A5100		RLB	F/R/P Barrier - SW No. 1	12d	Jul-21-14	Aug-05-...	18d
Stage 3A				105d	Apr-14-14	Sep-10...	0d
Roadwork				105d	Apr-14-14	Sep-10...	0d
A5590		SWPP	Install Stage 3A BMP's	5d	Apr-14-14	Apr-18-14	14d
A5630	4	RLB	Install Stage 3A ESA Fe...	5d	Apr-14-14	Apr-18-14	14d
A5570	76	RLB	Strip Existing Asphalt Fr...	1d	Apr-21-14	Apr-21-14	14d
A5580	76	ROCK	Break and Remove PC...	2d	Apr-22-14	Apr-23-14	15d
A5650	76	RLB	Strip Existing Asphalt Fr...	3d	Apr-22-14	Apr-24-14	14d
A5600		RLB	Rough Grade From Sta ...	3d	Apr-24-14	Apr-28-14	18d
A5660	76	ROCK	Break and Remove PC...	6d	Apr-25-14	May-02-...	14d
A5830		RLB	Install Underground Utilit...	4d	Apr-29-14	May-02-...	19d
A5610	101	RLB	Place Class II Base and...	3d	May-05-14	May-07-...	19d
A5680		RLB	Rough Grade From Sta ...	3d	May-05-14	May-07-...	14d
A5740	76	ROCK	Break and Remove PC...	6d	May-05-14	May-12-...	29d
A5620		RLB	Set Hubs/String Line an...	1d	May-08-14	May-08-...	21d
A5900		RLB	Install Underground Utilit...	5d	May-08-14	May-14-...	14d
A5940	104	OCJI	Pave AC From Sta. 178...	5d	May-09-14	May-15-...	21d
A5760		RLB	Rough Grade From Sta ...	2d	May-13-14	May-14-...	33d
A5820	76	ROCK	Break and Remove PC...	6d	May-13-14	May-20-...	29d
A5910		RLB	Install Underground Utilit...	3d	May-15-14	May-19-...	34d
A5960	112	RLB	Place Rebar from Sta. ...	3d	May-16-14	May-20-...	32d
A5640	112	RLB	Pave CRCP From Sta. ...	2d	May-21-14	May-22-...	36d
A5840		RLB	Rough Grade From Sta ...	2d	May-21-14	May-22-...	29d
A5930		RLB	Install Underground Utilit...	5d	May-23-14	May-30-...	29d
A7720		RLB	Profilograph CRCP Fro...	2d	May-23-14	May-27-...	62d
A5670	119	RLB	Pave JPCP From Sta. ...	4d	May-23-14	May-29-...	54d
A5690	101	RLB	Place Class II Base and...	4d	Jun-05-14	Jun-10-14	0d
A5700		RLB	Set Hubs/String Line an...	4d	Jun-11-14	Jun-16-14	0d
A5770	101	RLB	Place Class II Base and...	3d	Jun-11-14	Jun-13-14	19d
A5850	101	RLB	Place Class II Base and...	3d	Jun-16-14	Jun-18-14	19d
A5780		RLB	Set Hubs/String Line an...	2d	Jun-17-14	Jun-18-14	18d
A7390	104	OCJI	Pave AC From Sta. 170...	5d	Jun-17-14	Jun-23-14	0d
A5860		RLB	Set Hubs/String Line an...	2d	Jun-19-14	Jun-20-14	19d
A7400	104	OCJI	Pave AC From Sta. 166...	3d	Jun-24-14	Jun-26-14	15d

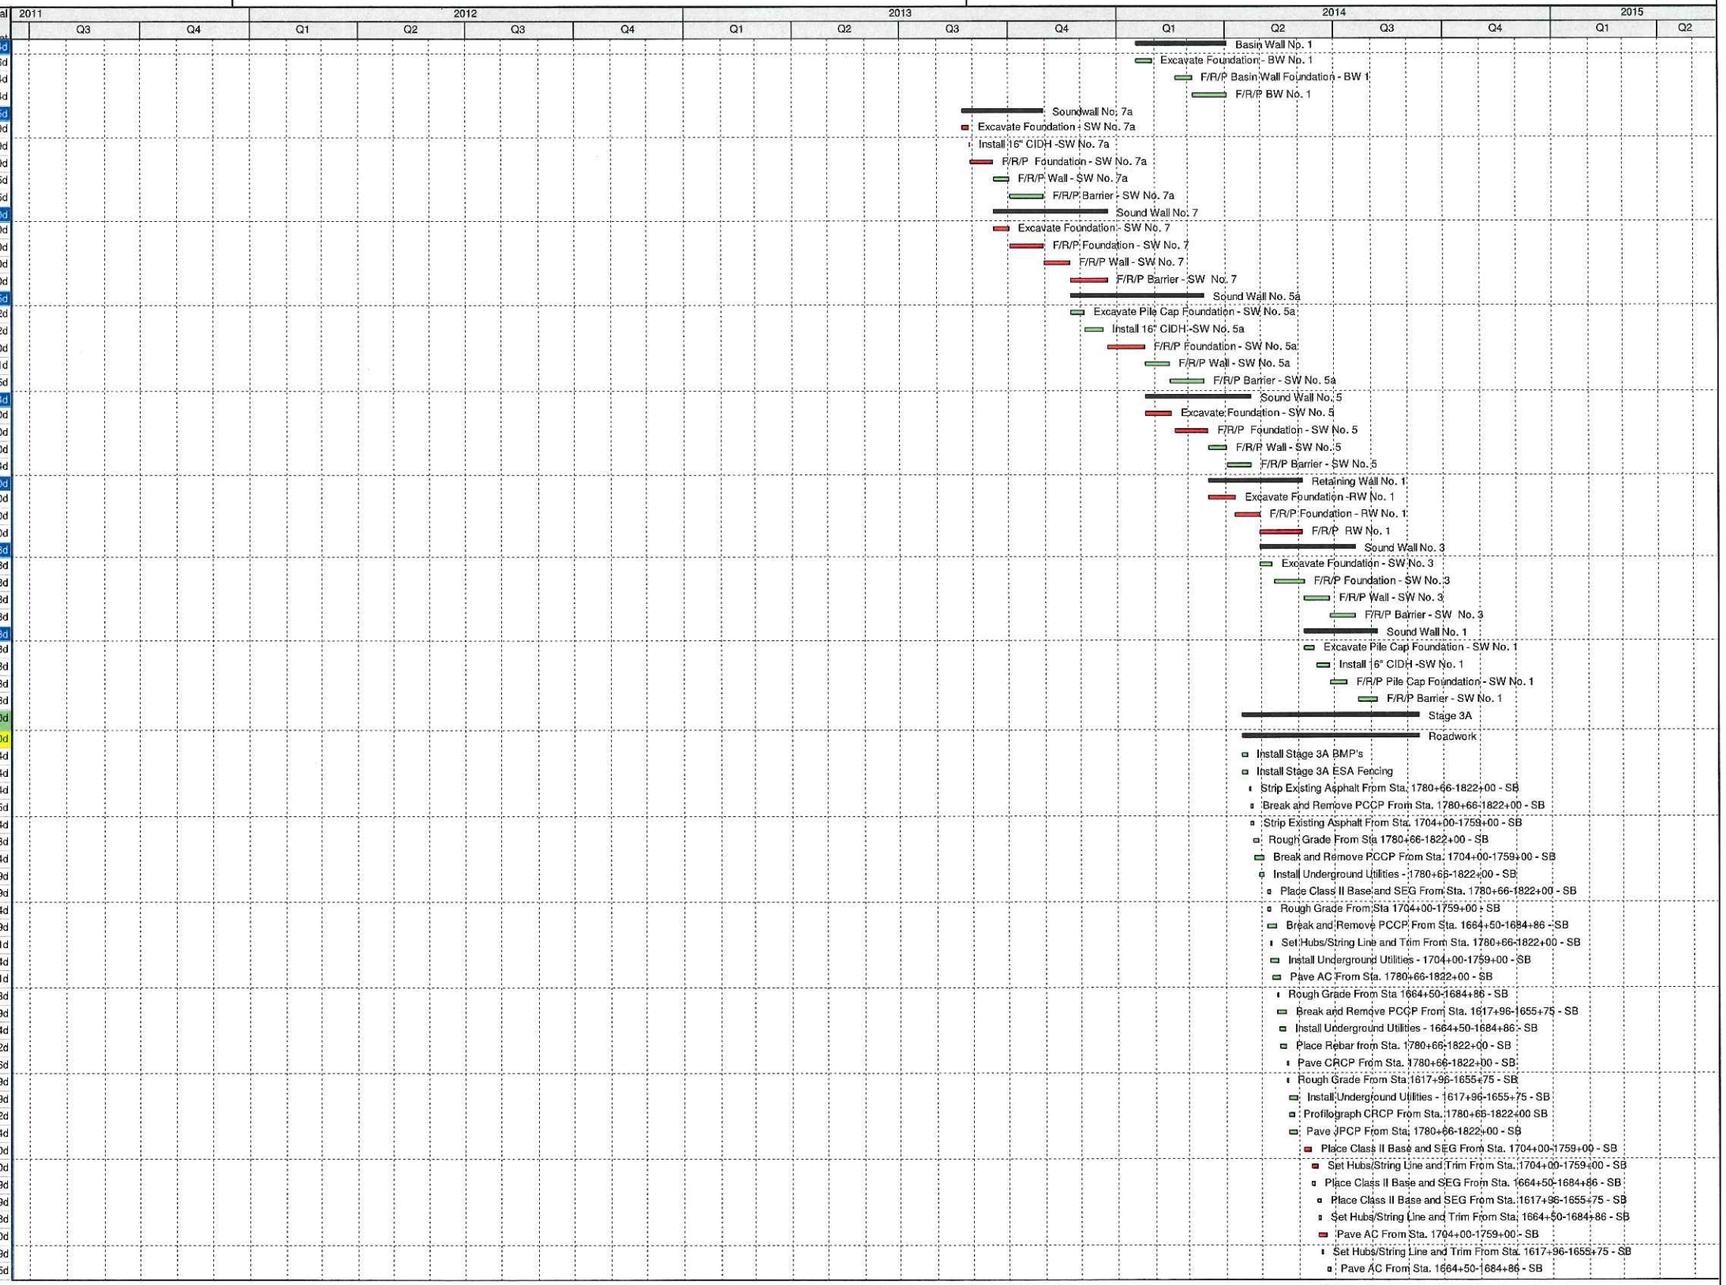

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Start Date: Jun-16-11

Activity ID	Bid Item	211080 - Group	Activity Name	OD	Start	Finish	Total Float
A7410	104	OCJI	Pave AC From Sta. 161...	4d	Jun-27-14	Jul-02-14	15d
A5710	112	CMCF	Place Rebar From Sta. ...	6d	Jul-08-14	Jul-15-14	0d
A5720	112	RLB	Pave CRCP From Sta. ...	6d	Jul-16-14	Jul-23-14	0d
A5790	112	CMCF	Place Rebar From Sta. ...	3d	Jul-16-14	Jul-18-14	4d
A5800	112	RLB	Pave CRCP From Sta. ...	3d	Jul-21-14	Jul-23-14	5d
A5870	112	CMCF	Place Rebar From Sta....	4d	Jul-21-14	Jul-24-14	4d
A7730		RLB	Profilograph CRCP Fro...	2d	Jul-24-14	Jul-25-14	22d
A5750	119	RLB	Pave JPCP From Sta. ...	4d	Jul-24-14	Jul-29-14	16d
A5880	112	RLB	Pave CRCP From Sta. ...	4d	Jul-25-14	Jul-30-14	4d
A7740		RLB	Profilograph CRCP Fro...	1d	Jul-28-14	Jul-28-14	22d
A5970	119	RLB	Pave JPCP From Sta. ...	3d	Jul-30-14	Aug-01-...	16d
A7750		RLB	Profilograph CRCP Fro...	2d	Jul-31-14	Aug-01-...	20d
A5990	119	RLB	Pave JPCP From Sta. ...	4d	Aug-04-14	Aug-07-...	16d
A6390		RLB	Finish Stage 3A	0d		Aug-29-...	0d
A6400		CRSP	Switch Traffic to Stage 3B	7d	Sep-02-14	Sep-10...	0d
Superstructure				69d	May-23-14	Aug-29-...	0d
A6200		RLB	Construct Approaches ...	4d	May-23-14	May-29...	42d
A6260		RLB	Construct Approaches ...	4d	May-30-14	Jun-04-14	45d
A5890		ACCW	Place Polyester Concre...	2d	May-30-14	Jun-02-14	42d
A6220		RLB	Construct Approaches ...	4d	Jul-24-14	Jul-29-14	0d
A6280		RLB	Construct Approaches ...	3d	Jul-24-14	Jul-28-14	9d
A6300		RLB	Construct Approaches ...	4d	Jul-29-14	Aug-01-...	9d
A6240		RLB	Construct Approaches ...	4d	Jul-30-14	Aug-04-...	0d
A5920		ACCW	Place Polyester Concre...	2d	Jul-30-14	Jul-31-14	2d
A6320		RLB	Construct Approaches ...	4d	Jul-31-14	Aug-05-...	4d
A5950		ACCW	Place Polyester Concre...	3d	Aug-05-14	Aug-07-...	0d
A6340		RLB	Construct Approaches ...	4d	Aug-06-14	Aug-11-...	4d
A5980		ACCW	Place Polyester Concre...	2d	Aug-08-14	Aug-11-...	0d
A6360		RLB	Construct Approaches ...	4d	Aug-12-14	Aug-15-...	4d
A6010		ACCW	Place Polyester Concre...	3d	Aug-12-14	Aug-14-...	0d
A6040		ACCW	Place Polyester Concre...	3d	Aug-15-14	Aug-19-...	0d
A6380		RLB	Construct Approaches ...	4d	Aug-18-14	Aug-21-...	4d
A6070		ACCW	Place Polyester Concre...	2d	Aug-20-14	Aug-21-...	0d
A6100		ACCW	Place Polyester Concre...	2d	Aug-22-14	Aug-25-...	0d
A6130		ACCW	Place Polyester Concre...	2d	Aug-26-14	Aug-27-...	0d
A6160		ACCW	Place Polyester Concre...	2d	Aug-28-14	Aug-29-...	0d
Walls				75d	Apr-14-14	Jul-29-14	23d
A5460	170	JJMM	Place Masonry Block - ...	6d	Apr-14-14	Apr-21-14	23d
A5480	170	JJMM	Place Masonry Block - ...	18d	Apr-22-14	May-15...	23d
A5500	170	JJMM	Place Masonry Block - ...	17d	May-16-14	Jun-10-14	23d
A5520	170	JJMM	Place Masonry Block - ...	6d	Jun-11-14	Jun-18-14	23d
A5540	170	JJMM	Place Masonry Block - ...	17d	Jun-19-14	Jul-14-14	23d
A5560	170	JJMM	Place Masonry Block - ...	11d	Jul-15-14	Jul-29-14	23d
Stage 3B				64d	Sep-02-14	Dec-04...	0d
Roadwork				57d	Sep-11-14	Dec-04...	0d
A6490		SWPP	Install Stage 3B BMP's	5d	Sep-11-14	Sep-17...	0d
A6470	76	RLB	Strip Existing Asphalt Fr...	2d	Sep-18-14	Sep-19...	0d
A6480	76	ROCK	Break and Remove PC...	4d	Sep-22-14	Sep-25...	0d
A6550	76	RLB	Strip Existing Asphalt Fr...	3d	Sep-22-14	Sep-24...	1d
A6630	76	RLB	Strip Existing Asphalt Fr...	3d	Sep-25-14	Sep-29...	1d
A6500		RLB	Rough Grade From Sta ...	2d	Sep-26-14	Sep-29...	4d
A6560	76	ROCK	Break and Remove PC...	6d	Sep-26-14	Oct-03-14	0d
A6640	76	ROCK	Break and Remove PC...	6d	Sep-30-14	Oct-07-14	1d
A6950		RLB	Install Underground Utilit...	3d	Sep-30-14	Oct-02-14	6d
A6510	101	RLB	Place Class II Base and...	3d	Oct-03-14	Oct-07-14	6d
A6580		RLB	Rough Grade From Sta ...	2d	Oct-06-14	Oct-07-14	0d
A6520		RLB	Set Hubs/String Line an...	1d	Oct-08-14	Oct-08-14	6d
A6660		RLB	Rough Grade From Sta ...	2d	Oct-08-14	Oct-09-14	1d
A6720	76	ROCK	Break and Remove PC...	4d	Oct-08-14	Oct-14-14	3d
A7270		RLB	Install Underground Utilit...	4d	Oct-08-14	Oct-14-14	0d
A7420	104	OCJI	Pave AC From Sta. 181...	2d	Oct-09-14	Oct-10-14	6d
A7280		RLB	Install Underground Utilit...	4d	Oct-10-14	Oct-16-14	1d
A6530	112	CMCF	Place Rebar From Sta. ...	3d	Oct-14-14	Oct-16-14	6d
A6590	101	RLB	Place Class II Base and...	3d	Oct-15-14	Oct-17-14	0d
A6740		RLB	Rough Grade From Sta ...	2d	Oct-15-14	Oct-16-14	3d
A6540	112	RLB	Pave CRCP From Sta. ...	3d	Oct-17-14	Oct-21-14	6d
A6670	101	RLB	Place Class II Base and...	3d	Oct-17-14	Oct-21-14	1d
A7290		RLB	Install Underground Utilit...	3d	Oct-17-14	Oct-21-14	3d
A6600		RLB	Set Hubs/String Line an...	2d	Oct-20-14	Oct-21-14	0d
A6680		RLB	Set Hubs/String Line an...	2d	Oct-22-14	Oct-23-14	1d
A6750	101	RLB	Place Class II Base and...	3d	Oct-22-14	Oct-24-14	3d
A7430	104	OCJI	Pave AC From Sta. 175...	3d	Oct-22-14	Oct-24-14	0d

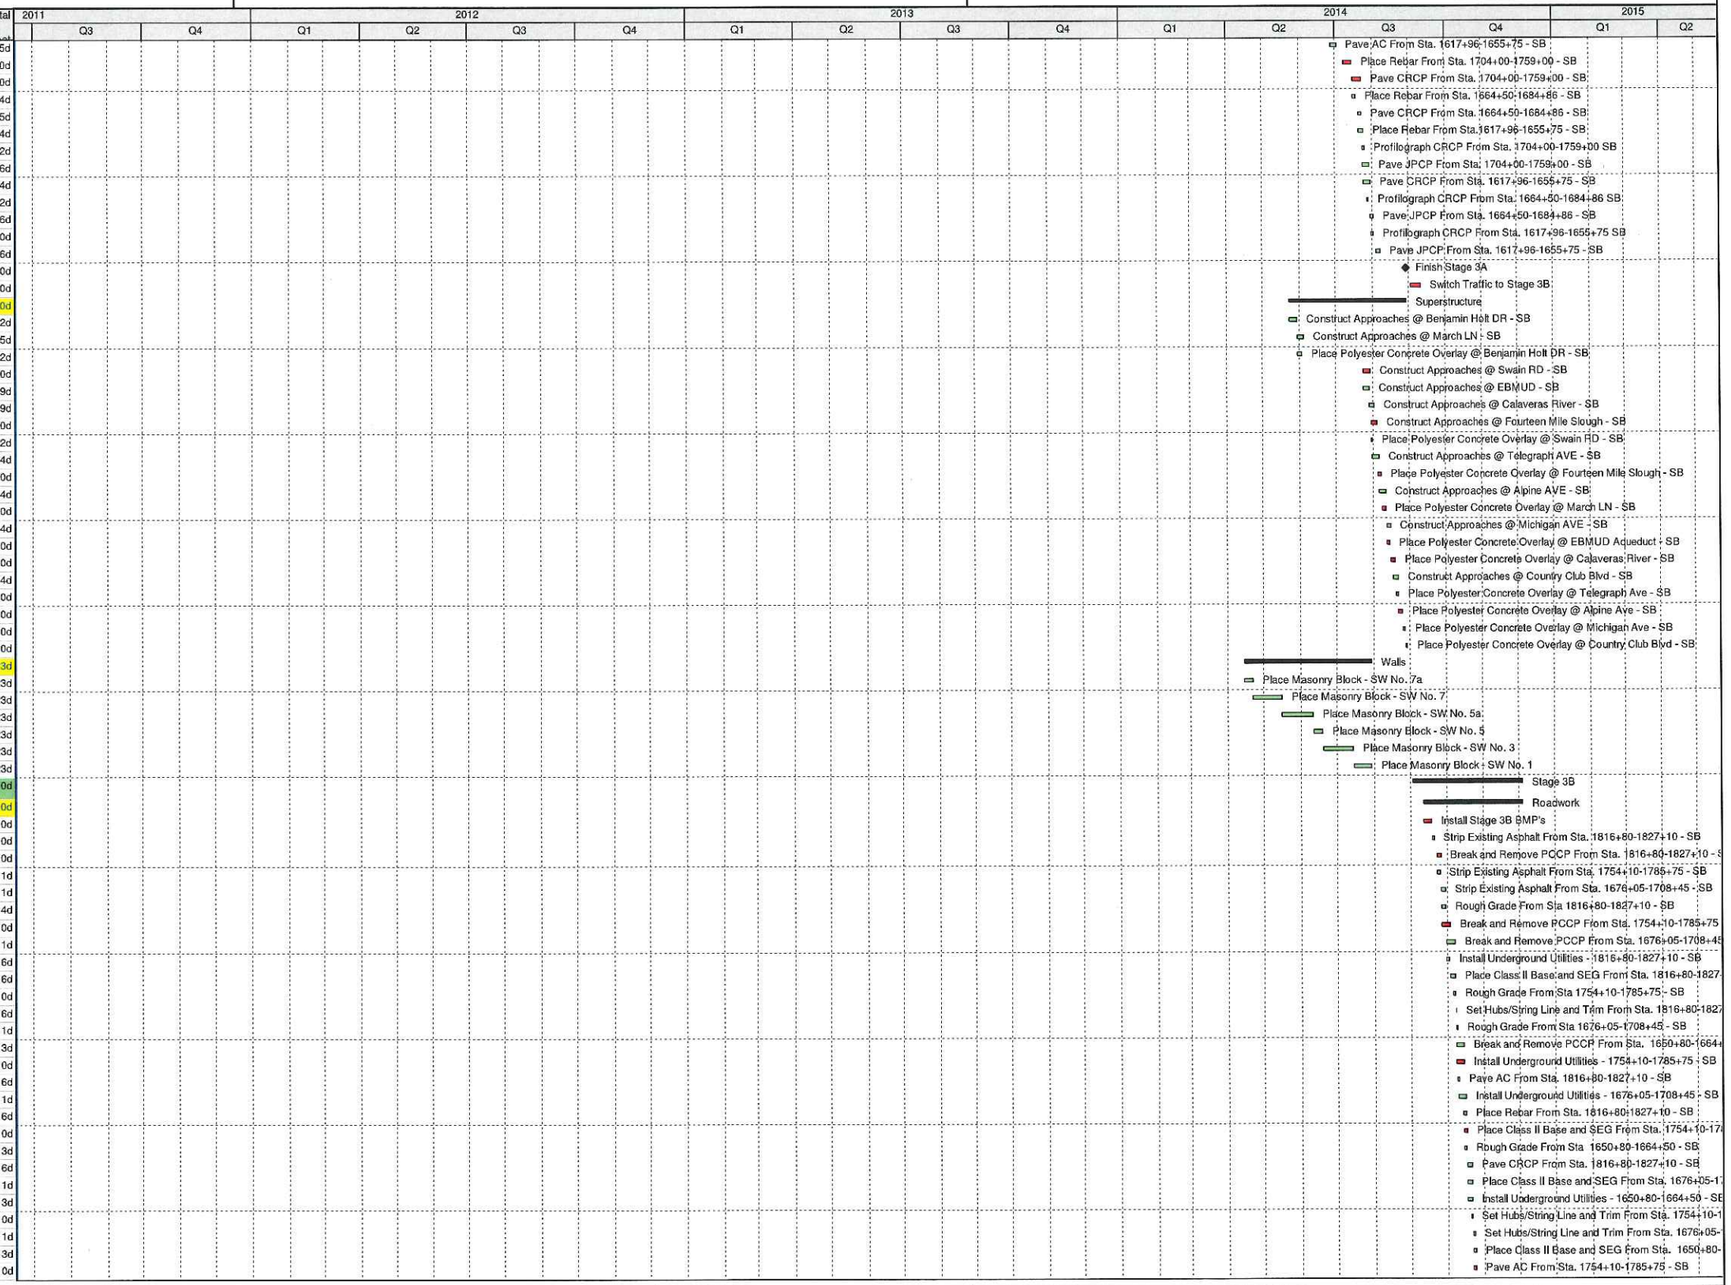

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Start Date: Jun-16-11

Activity ID	Bid Item	211080 - Group	Activity Name	OD	Start	Finish	Total Float
A7760		RLB	Profilograph CRCP Fro...	1d	Oct-22-14	Oct-22-14	19d
A6570	119	RLB	Pave JPCP From Sta. ...	3d	Oct-22-14	Oct-24-14	10d
A7440	104	OCJI	Pave AC From Sta. 167...	3d	Oct-24-14	Oct-28-14	1d
A6610	112	CMCF	Place Rebar From Sta. ...	3d	Oct-27-14	Oct-29-14	0d
A6760		RLB	Set Hubs/String Line an...	1d	Oct-27-14	Oct-27-14	3d
A7450	104	OCJI	Pave AC From Sta. 165...	2d	Oct-28-14	Oct-29-14	3d
A6620	112	RLB	Pave CRCP From Sta. ...	3d	Oct-30-14	Nov-03...	0d
A6690	112	CMCF	Place Rebar From Sta. ...	3d	Oct-30-14	Nov-03...	0d
A6700	112	RLB	Pave CRCP From Sta. ...	3d	Nov-04-14	Nov-06...	0d
A6770	112	CMCF	Place Rebar From Sta. ...	3d	Nov-04-14	Nov-06...	0d
A7770		RLB	Profilograph CRCP Fro...	1d	Nov-04-14	Nov-04...	11d
A6650	119	RLB	Pave JPCP From Sta. ...	4d	Nov-04-14	Nov-07...	4d
A6780	112	RLB	Pave CRCP From Sta. ...	3d	Nov-07-14	Nov-12...	0d
A7780		RLB	Profilograph CRCP Fro...	2d	Nov-07-14	Nov-10...	9d
A6730	119	RLB	Pave JPCP From Sta. ...	4d	Nov-10-14	Nov-14...	4d
A7790		RLB	Profilograph CRCP Fro...	1d	Nov-13-14	Nov-13...	8d
A6790	119	RLB	Pave JPCP From Sta. ...	3d	Nov-17-14	Nov-19...	4d
A6830		RLB	Finish Stage 3B	0d		Nov-25...	0d
A6840		CRSP	Switch Traffic to Stage 4	5d	Nov-26-14	Dec-04...	0d
Superstructure				59d	Sep-02-14	Nov-25...	0d
A6420		ACCW	Place Joint Seal @ Cou...	3d	Sep-02-14	Sep-04...	29d
A8160	174	ACCW	Place Joint Seal @ Mic...	3d	Sep-05-14	Sep-09...	29d
A8170	173	ACCW	Place Joint Seal @ Alpi...	3d	Sep-10-14	Sep-12...	29d
A8190	175	ACCW	Place Joint Seal @ Cal...	3d	Sep-15-14	Sep-17...	29d
A8210	173	ACCW	Place Joint Seal @ Mar...	3d	Sep-18-14	Sep-22...	29d
A8220	173	ACCW	Place Joint Seal @ Fou...	3d	Sep-23-14	Sep-25...	29d
A8230	173	ACCW	Place Joint Seal @ Swa...	3d	Sep-26-14	Sep-30...	29d
A8240	173	ACCW	Place Joint Seal @ Benj...	3d	Oct-01-14	Oct-03-14	29d
A6800		RLB	Construct Approaches ...	3d	Nov-07-14	Nov-12...	6d
A6820		RLB	Construct Approaches ...	3d	Nov-13-14	Nov-17...	6d
A6440		ACCW	Place Polyester Concre...	1d	Nov-13-14	Nov-13...	0d
A6410		ACCW	Place Polyester Concre...	2d	Nov-14-14	Nov-17...	0d
A8180	173	ACCW	Place Joint Seal @ Tele...	3d	Nov-18-14	Nov-20...	0d
A8200	173	ACCW	Place Joint Seal @ EB...	3d	Nov-21-14	Nov-25...	0d
Stage 4				55d	Dec-05-14	Feb-26-...	54d
Roadwork				55d	Dec-05-14	Feb-26-...	54d
A6860	224	CMCF	Layout Rebar for Media...	10d	Dec-05-14	Dec-18...	12d
A6880		GERC	Install Overhead Sign St...	15d	Dec-05-14	Dec-26...	20d
A6890		CENF	Restore Guardrail @ So...	5d	Dec-05-14	Dec-11...	104d
A7140		SWPP	Install Stage 4 BMP's	5d	Dec-05-14	Dec-11...	0d
A6850		RLB	Set String Line for Medi...	10d	Dec-12-14	Dec-26...	0d
A6870	224	RLB	Slip Barrier	20d	Dec-29-14	Jan-27-15	0d
A6900		RLB	Remove K-Rail	10d	Jan-28-15	Feb-10-...	0d
A6910		OCJI	Overlay Local Detour R...	5d	Feb-11-15	Feb-19-...	59d
A7300		CRSP	Final Stripe	10d	Feb-11-15	Feb-26-...	0d

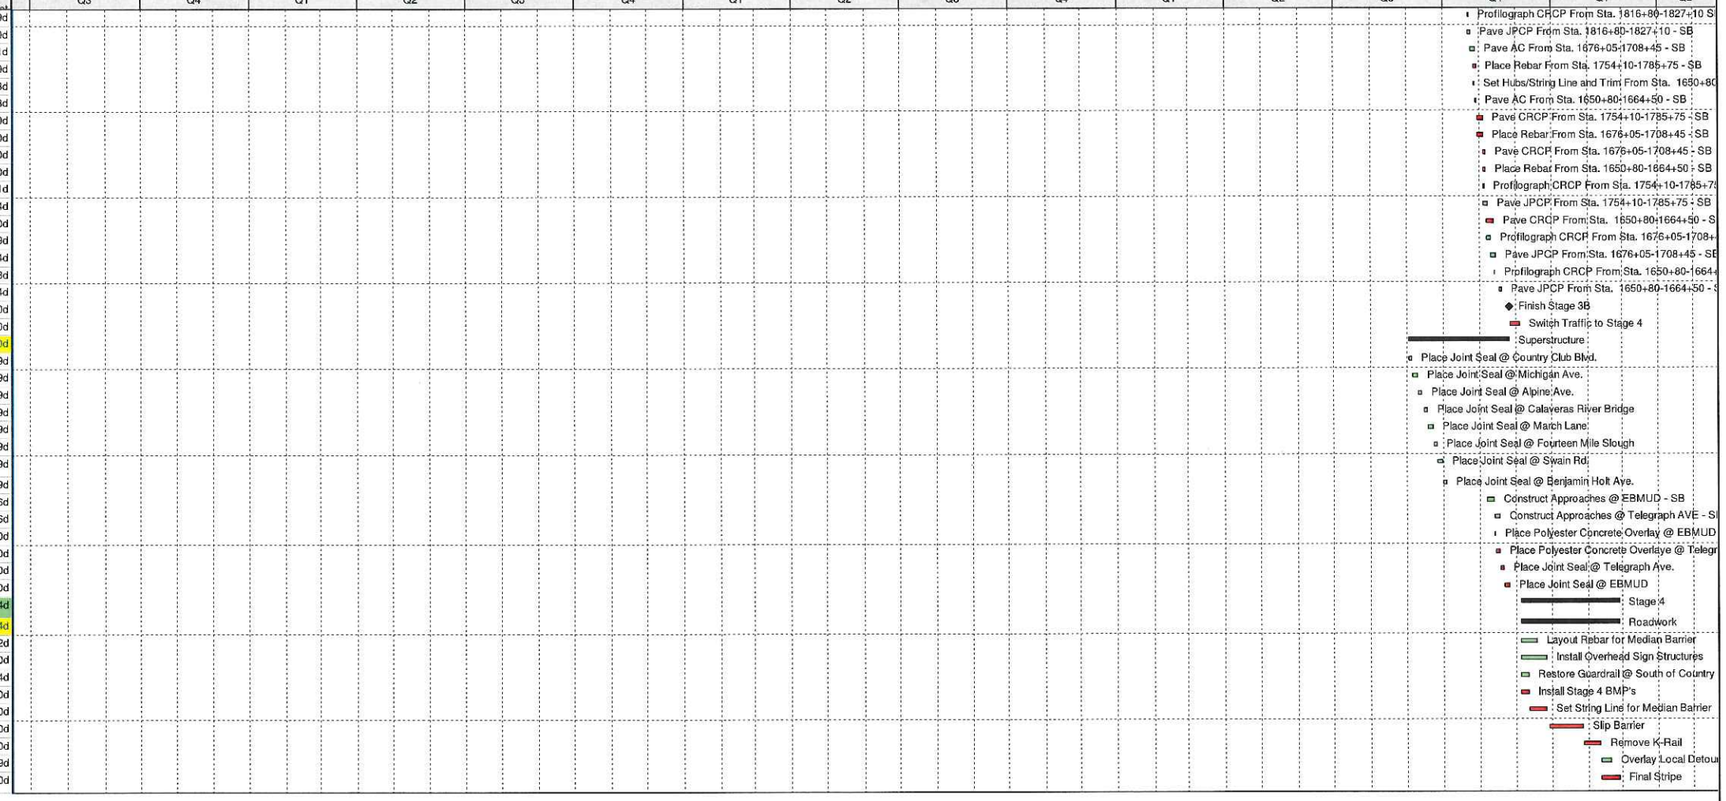

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Start Date: Jun-16-11
