SIGNS BEING USED

48X48" C30A-CA

48X48" C24-CA

48X48" W20-1

R30 24X24" BARRICADE MOUNTED, PLACED ON BOTH SIDES OF STREET 20' APART 72HR PRIOR TO START OF WORK

TOW-AWAY ZONE

ADDITIONAL TRAFFIC CONTROL PERSON TO MAINTAIN CLOSURE AND ASSIST BICYCLE, PEDESTRIAN AND DRIVE WAY TRAFFIC SHOULD NEED ARISE

FOR TCP QUESTIONS CALL:
ROBERT @ 209-200-3351

SEE SPEC SHEET 2 FOR ADDITIONAL TRAFFIC CONTROL STIPULATIONS

PEDESTRIAN AND BICYCLE ACCESS TO REMAIN OPEN AT ALL TIMES

WORK SHALL NOT EXCEED 12HRS

MIN 12' CLEARANCE FOR TRAFFIC

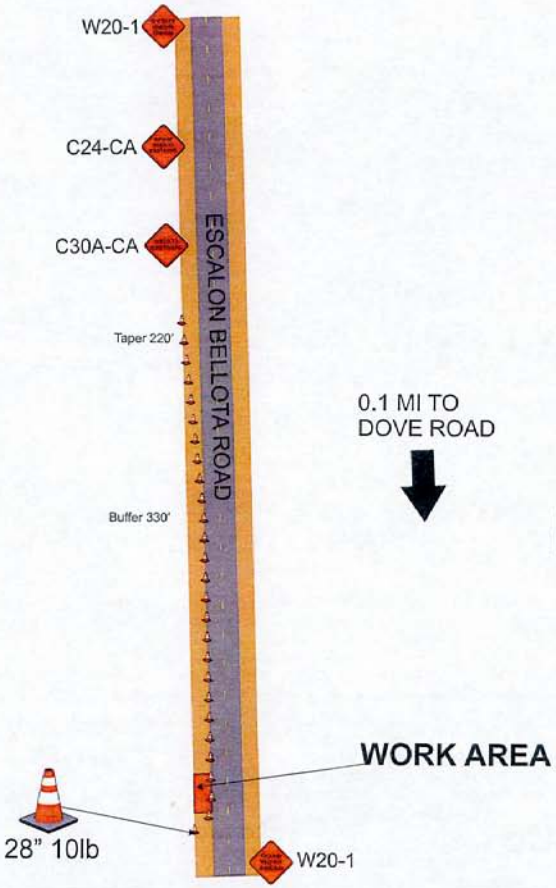

TRAFFIC CONTROL ZONES

SPEED	TAPER	BUFFER	SIGN SPACING	MAX CONE SPACING TAPER	MAX CONE SPACING TANGENT
25	125'	60'	100'	25	50
30	180'	90'	250'	30	60
35	245'	120'		35	70
40	320'	160'		40	80
55	660'	300'	500'	55	110

LOC 1
NOT: 107997951

C17(CA)



Placed at each W20-1

ELEC
NOT TO SCALE

PM 31079522

Owner: COUNTY OF SAN JOAQUIN	
Project Location: Escalon Bellota Rd @ Dove Rd	Project City: Escalon , CA
Prime Contractor: PG&E	Traffic Control Contractor: ED SAFETY INC
Phone: 209-333-0807 / Sheet Number: PS-1	Date: 7/14/2014
Prepared By: ED SAFETY SERVICES, INC	

HOURS OF WORK SHALL BE DETERMINED BY THE COUNTY OF SAN JOAQUIN
