OCalcDataForm 8A_G100852_20150616_145442

Date	**2015-06-16**
Pole ID	**102136519**
Pole Type	**Type 3**
Pole Class	**4**
Species	
Pole Length	**45**
Truck Access	**Yes**
Vegetation Needed	**No**
Traffic Control	**No**
Circumference	**40**

Target Location	
ImageFilename	**Target Location_G100852_20150616_143452.jpg**
Distance	**101'4"**
TrueBearing	**2.4°**
TargetLatitude	**37.880990528°**
TargetLongitude	**-121.276036090°**
TargetAltitude	**29'8"**

SIGNS BEING USED

- 48X48" W4-2R
- 48X48" W20-5R
- 48X48" C30 (CA)
- 48X48" W20-1
- 48X48" W11-1
- W16-1

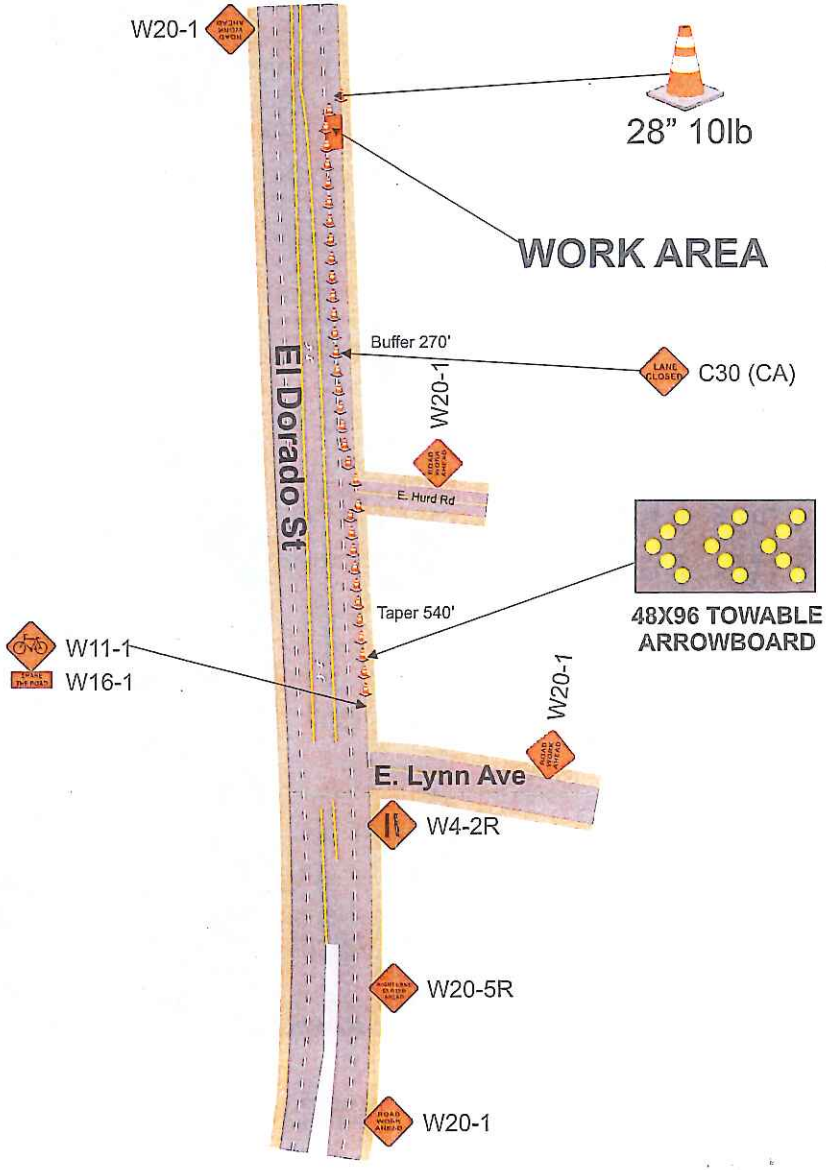

mph	feet			
SPEED	TAPER	SIGN SPACING	TAPER	TANGENT
25	125'	100'	25	50
30	180'	250'	30	60
35	245'		35	70
40	320'		40	80
45	540	350'	45	90
50	600'		50	100
BUFFER(1/2taper)		SHOULDER(1/3taper)		

N W E S

WORK ZONE
SPEED LIMIT 35

G20-5aP & R2-1 Barricade Mounted, placed with each W20-1 Sign

TOW-AWAY ZONE

R30 24X24" Barricade mounted, placed on both sides of the street 20' apart 72HR prior to start of work.

For TCP questions call
ROBERT @ 209-200-3351

SEE SPEC SHEET 2 FOR ADDITIONAL TRAFFIC CONTROL STIPULATIONS

Pedestrian and Bicycle Access to remain open at all times.

Minimum 12ft clearance for traffic

Work shall not exceed 12 hours

NOT TO SCALE

HOURS OF WORK SHALL BE DETERMINED BY SAN JOAQUIN COUNTY

PM# 31140336

Owner	SAN JOAQUIN COUNTY	
Project Location		Project City
8260 El Dorado St		French Camp, CA
Prime Contractor		Traffic Control Contractor
PG&E		City Rise Services, Inc.
Phone	Sheet Number	Date
209-333-0807	PS-1	6/25/2015
Prepared By	CITY RISE SERVICES, INC	
